

Somalia Urban Resilience Project Phase II, NAGAAD (P170922)
Mid-Term Review (MTR) Mission
October 29th – November 17th, 2024
AIDE MEMOIRE

I. INTRODUCTION

1. A World Bank team¹ conducted a Mid-Term Review from October 29th – November 17th, 2024, in Nairobi, Garowe, and virtually. The main objectives: (i) to assess project design and implementation progress towards achieving the Project Development Objectives; (ii) discuss detailed work plans, institutional arrangements, progress on the results framework, and disbursement targets; (iii) review fiduciary and environmental and social framework (ESF) compliance; (iv) agree on course corrections and next steps for improving project performance; and (v) discussion with Hargeisa city. Additionally, conduct technical discussions on the ongoing preparatory diagnostics for the proposed Somalia Informal Settlements Upgrading Project.

2. The team would like to thank the Minister, State Minister, and Director General (DG) of the federal Ministry of Public Works, Reconstruction and Housing (MPWRH), Federal State Minister MPWRH, Mayors from participating cities, Project Coordination Unit (PCU), Project Implementation Units (PIUs) of participating cities, United Nations Office for Project Services (UNOPS), and International Organization for Migration (IOM), representatives from the European Union (EU), Germany Kreditanstalt für Wiederaufbau (KfW), and Foreign, Commonwealth, and Development Office, UK (FCDO). This Aide Memoire summarizes the key findings, recommendations, and agreements reached during the MTR. Table 1 shows key project data. As agreed during the meetings with the Government, this Aide Memoire is classified as an official document as required by the World Bank Access to Information Policy.

Table 1. Key project data

Board Date	December 2019
Effectiveness	March 2020
Additional Financings (AFs)	AF1 US\$21.5M – June ‘22, Effective July ‘22 AF2 US\$50M – Approved Jan ‘23, Effective Apr ‘23 AF3 US\$50M – Approved May ‘24, Effective Aug ‘24
IDA and MPF TF	IDA: US\$ 160M; MPF: US\$ 93.5M Total: US\$253.5 million
Total Disbursement as at MTR	IDA: US\$ 71.41M (44%); MPF: US\$50.76M (54%); Total: 122.17 (48%)
Total Commitments as at MTR	US\$152M (60%) of total project allocation
Expected Total Disbursement -Dec’25	US\$194M
Project Development Objective Rating	Satisfactory – remains the same as previous mission
Implementation Progress Rating	Satisfactory – upgraded from Moderately Satisfactory
Closing Date	December 31, 2026

¹ The Mission comprised: Nandya Thalyta Yuwono (Sr. Urban Specialist, Task Team Leader [TTL]) and Benjamin Kushner (DRM Specialist/Co-TTL), Soraya Goga (Lead Urban Specialist), Samuel Mbachia (Engineer Consultant), Stephen Amayo (Sr. Financial Management Specialist), Francis Muthuiya (Sr. Procurement Specialist), Abdirahman Zeila (Sr. Environment Specialist), Jacinta Murunga (Social Development Specialist), Samantha Wijesundera (Engineer, Consultant), Nisha Pinho (WFA, Finance Analyst), Miguel De Corral (Sr. Operations Officer), Adam Diehl (Sr. Transport Specialist), Melody Benavidez (Urban Resilience Consultant), Sarah Cramer (M&E Consultant), Fathi Egal (Consultant), Nancy Muthoni (Team Assistants).

II. KEY AREAS FOR ATTENTION

3. **Accelerating project implementation.** With current project closing date of December 31, 2026, the mission identified actions needed for expediting physical progress, particularly in Dhusamareb, Beledweyne, and Mogadishu. For Mogadishu, roads contracts will be awarded by December 2024. Beledweyne and Dhusamareb have initiated procurement process and will award contract for their first construction packages by February 2025. Key actions include monthly check-ins with each city and UNOPS and updating the Management Information System (MIS) on progress of activities in each city. Third party monitoring will commence in June 2025 for semi-annual continuous activity moving forward.

4. **Ensure timely payments and accelerating disbursement.** As the project approaches its closing date in two years' time, disbursement stands at US\$122.03 million or around 48%, and around 60% committed. Projected disbursement between December 2024 and December 2025 approximately US\$65 million, and payments ready for submission to the Bank by December 2024 stands at US\$8 million. The mission noted there was payment delay in Garowe, Puntland for UNOPS. This issue was resolved during the mission. For future payments, similar issue may arise. The team recommends for the government led by MPWRH to make an agreement with Puntland EAFS for way forward to ensure timely payment. It was agreed during the mission that the PCU FM specialist will facilitate monthly check-in with each PIU FM specialist, to ensure timely submission of payments.

5. **Strengthening contract management.** Contract management remains an issue. To bolster the PIUs capacity around contract management a training was held for PCU and PIUs, prior to the MTR. A new mitigation plan was agreed during the mission, which will include joint contract management plans and contract registers between the project teams and UNOPS to ensure parties meet their obligations. The PCU will continue to convene monthly 'check-ins' with each PIU and UNOPS to review progress, which will also be informed by monthly progress reports and in the Management Information System (MIS).

6. **Building institutional capacity for sustainability.** The mission highlighted the importance of further building the capacity at multiple levels of government to support delivery of municipal services and for sustainability of investments initiated under the project. This includes federal level MPWRH and federal member state (FMS) level, although not overtaking the implementation function of the municipal governments.

- **Capacity building for FGS and FMS MPWRH** will be a joint effort with the Somalia Horn of Africa Infrastructure Integration Project (SHIIP) and mobilizing other resources, such as the Programmatic Analytical and Advisory Services (PASA) Livable Cities and Disaster Resilience Platform.
- **Capacity building for municipal staff.** Participating cities through the PIU will prepare a proposal for targeted capacity building for operations and maintenance for municipal staff and FMS MPWRH engineers, as well as proposed list of equipment and/or tools needed for O&M. PCU will facilitate consultation process with FGS and FMS MPWRH for the proposed capacity building need. The first consultation will be in the second week of December as part of the agenda for monthly check-in.
- **Capacity building for PCU and PIUs.** The mission noted there is a need for strengthening communications and capacity of PCU and PIUs on project management. Team building and

targeted capacity building need will be discussed in the next monthly check-in with the Bank. In person team building for PCU and PIUs will be scheduled for the last week of January 2025.

7. **Completion of Component 4. Urban Forced Displacement and drought response activities by IOM.** This component has been successfully completed. It was discussed during the mission that IOM will act on design issue with Baidoa temporary shelter during the Defect Liability Period (DLP). In addition, IOM will provide clear timeline for data sharing with the MPWRH by using similar process as Baxnaano project by December 19, 2024. This will include agreement to have additional agreement with the MPWRH on data sharing. As agreed during the mission, submission of the final report for the overall activities will be submitted to the MPWRH through the PCU by December 31, 2024.

8. **Potential of project restructuring to add Hargeisa.** During the MTR mission, the team noted that a request for additional financing to add Hargeisa is under discussion. This will require a project restructuring, additional financing, and possible extension of project closing date, see Section VI for more detail. This will require a separate assessment with Hargeisa team, and this is scheduled for virtual meetings on the second week of December 2024. An official request letter is expected to be shared with the Bank by December 9, 2024.

9. **Proposed Somalia Informal Settlements Upgrading Project.** The World Bank, together with MPWRH, the Project Coordination Unit (PCU), Project Implementation Unit (PIU), U.N agencies, MOPIED Durable Solutions Unit, discussed technical aspects of project preparation for the Somalia Informal Settlement Upgrading Project (SISUP). These discussions were led by thematic experts and covered critical areas, including the role of urban upgrading, sites and services and rental housing in the housing value chain, settlement typology and selection, options for infrastructure and service delivery (including social enterprises), livelihoods and job creation and environmental and social frameworks pertinent to urban upgrading and housing. The proposed Project timeline includes a Project Concept Note this Fiscal Year (ending June 2025), followed by a targeted project approval in Q1/Q2 next FY (the Bank's FY starting July 2025). To facilitate Project preparation, the mission discussed with the MPWRH on an updated request letter for the Project from the Ministry of Finance and for stakeholder consultations planned for January 2025.

10. **Programmatic Analytical and Advisory Services (PASA) Livable Cities and Disaster Resilience Platform.** The mission also introduced the *Livable Cities Platform* PASA. Designed with an implementation over 3 years, the PASA will undertake analytics and technical assistance under 5 pillars. These include: (i) Disaster and Climate Risk Management; (ii) Inclusive Cities; (iii) Urban Services; (iv) Competitive Cities; and (v) Alternative financing for municipal governments. Building on insights from the Somalia Urbanization Review, PASA will enhance diagnostic capacity, inform long-term urban strategy, and support the ISU's policy dialogue and preparatory work. As initial engagements, the Client and the Team agreed on the need for Housing and Land Policy Dialogue, Settlements and Spatial Analytics in key cities – including a mapping of public land in Mogadishu and selected cities.

III. SURP-II IMPLEMENTATION PROGRESS AND KEY FINDINGS

Overall implementation progress:

11. **Implementation progress and assessment of project design at MTR.**

- **Project Development Objective.** The PDO of the project is “*to strengthen public service delivery capacity of local governments, increase access to climate-resilient urban infrastructure and services, and to provide immediate and effective response to an eligible crisis or emergency in selected areas.*” The PDO and its indicators remain highly relevant and achievable. The project aims to provide 1 million people with improved access to climate-resilient urban infrastructure and services and has already exceeded 1 million beneficiaries, of which a significant proportion are women and IDPs.
- **Performance towards achieving PDO and Implementation Progress (IP).**
 - The progress towards achievement of PDO remains *Satisfactory*.
 - The performance of IP upgraded as *Satisfactory*. The mission acknowledged significant improvement on implementation progress and disbursement. Further, the mission acknowledged full compliance of ESF, PCU and PIUs are fully staffed and budgeted, three out of four PDO indicators have been achieved, and Component 4. Urban Forced Displacement successfully completed.
- **Disbursement trend.** As of November 18, 2024, cumulative disbursement stands at US\$122.03 million, representing approximately 48 percent of the total budget of US\$253.5 million with approximately 60 percent committed. The disbursement has increased by US\$27.36 million in 6 months since the previous ISM in May 2024.
- **The use of country system and performance-based allocation.** The mission acknowledged that one of the achievements of the project is the use of country system on the allocating funds to participating cities. On implementation, cities are responsible for implementing the project, including participatory planning and consultations, procurement, supervision, and adopting operations and maintenance manual.
- **Institutional strengthening and capacity building.** This is key to the success of project implementation in Somalia. The project started with capacity building to the PCU and PIUs. At MTR, the mission noted that there has been transfer of knowledge and trainings to municipal staff and peer learning from other projects.
- **U.N agencies to support project implementation.** The project, through the government of Somalia, contracted the United Nations Office for Project Services (UNOPS) to support the PIU on supervision of civil works. In addition, UNOPS provided design for infrastructure investments and capacity building program for the PIUs and municipal staff for sustainability. The MTR mission acknowledge the importance of continuing with this model throughout the project.

Implementation progress by Component:

Component 1: Urban Infrastructure and Services (US\$155 million)

12. This component is expected to provide feasibility studies and designs for resilience urban infrastructure, followed by civil works. The number and size of infrastructure investments in each city varies, depending on city allocation formula agreed in the beginning of the project. The implementation of this component is on track. The cities started their proposed investments on roads with side drainage, pedestrian walks, and streetlights. Garowe, Baidoa, and Kismayo have completed their initial roads packages. Mogadishu will award its roads packages by December

2024, while Dhusamareb and Beledweyne are expecting to award their first civil works contract by February 2025. This is on schedule, as agreed in May ISM².

13. **Roads, side drainage, pedestrian walkways.** Civil works for roads package 1 in Garowe, Kismayo, Baidoa and Mogadishu have been completed.³ Various quick disbursing activities planned in Mogadishu⁴ have also been completed. While package 2 works in Garowe and the construction of Dhusamareeb, Beledweyne and BRA PIU office are on schedule. Progress of work gained momentum in the last four months as contractor increased resources and completed asphalt works. Works are slightly delayed in Kismayo.⁵ Delays are attributed to late mobilization of key equipment and materials, breakdown of equipment, contractor's poor cashflow, and heavy rains, award of multiple contracts resulting in sharing of resources, and limited contractors' contract management capacity. The PIUs will ensure that contractors update their work program and prepare recovery plans to ensure timely completion. In Kismayo, package 3 construction of 5.1km AC roads, two detention ponds and drainage outfall will start in January 2025, and Baidoa will package 3A and 3B construction of 2.5Km and 4.1Km AC roads will start in February and April 2025 respectively. In Mogadishu, BRA has prepared feasibility study report and designs for citywide trunk drainage and 13km urban roads are ongoing with UNOPS, while procurement of condition assessment and cleaning of 5km existing drainage and construction of PIU office is progressing well. Construction of Dhusamareeb PIU office and materials testing laboratory is progressing well, and Beledweyne has commenced construction of PIU office and laboratory in October 2024.

14. **City-wide drainage.** UNOPS was initially contracted by the project to prepare roads design and supervision for civil works contracts. For AF3 activities, UNOPS will provide feasibility studies and designs of citywide drainage in Mogadishu and Garowe, as well as urban roads in Beledweyne⁶ and Dhusamareeb. Preparation of priority investments with the new allocation from AF3 have commenced in all cities with Kismayo most advanced with ready designs for 5.1km roads, associated drainage, two detention ponds and three outfalls. Mogadishu, Dhusamareeb and Beledweyne have completed designs and bidding documents for priority investments in November 2024, while designs for Garowe and Mogadishu package 1 citywide drainage will be ready by December 2024 and March 2025 respectively. In December 2024, Baidoa will engage UNOPS for feasibility studies and design of citywide drainage and gravel link road. To ensure timely delivery in each city, UNOPS has engaged additional experts to undertake some designs in-house, and experienced firms for specialized design of bridges and citywide drainage. UNOPS has agreed with PCU and PIUs on detailed timelines for deliverables in each city to ensure to avoid further slippage and ensure timely implementation of AF3 investments.

Component 2: Institutional Strengthening and Analytics (US\$3 million)

15. **Progress to Date.** The component has provided technical assistance to strengthen core municipal functions through technical assistance on informal settlements (for Baidoa, Garowe, Mogadishu), climate-resilient operation, and maintenance (O&M) (for Mogadishu), solid waste

² Of a total of 96.7km roads with drainage, 32.3km (33.5%) asphalt concrete roads with drainage and outfall completed, 9.9km (10.2%) and a 145m bridge ongoing, 14.96km (15.5%) at different procurement stages, designs for 30.5km (31.5%) are ready for procurement and works to start in between March and June 2025, and designs for 9km (9.3%) gravel road will be complete in March 2025 for works to start in July 2025.

³ A total of 32.3km asphalt concrete (AC) roads have been completed; in Garowe – 9.1km, Kismayo – 8.3km and 750m outfall drainage, Baidoa – 14.7km, and Mogadishu 0.23km.

⁴ Quick wins include: i) construction of the Ceymiska Road (230m, B15); ii) drainage extension of Tabeelaha Jaceylka Road (255m, B20); iii) dredging of 4 catchment ponds (Bondhere, Hillac, Tunbluq and 15th May catchments) to improve urban flood management; and iv) women's skills training.

⁵ Construction of 21.5Km of roads with drainage is ongoing: works in Garowe are 95% progress vs 97% time for 145m long bridge and 1.22km AC road, works in Baidoa are 95% progress vs 99% time spent for 10.8km AC roads, and are delayed in Kismayo 65.1% progress vs 87% time for 4.75km roads and 8.5% vs 34% time for 4.5km roads. Asphalt concrete (AC) roads include side drainage, pedestrian sidewalk, some streetlighting, and two detention ponds in Kismayo.

⁶ UNOPS TA will also support feasibility study and design of two new bridges and assessment of two existing bridges in Beledweyne.

management (for Mogadishu), flood risk management (for Kismayo, Garowe), Nature Based Solutions Opportunity Scans (NBSOS) and a mayors' forum. The project is also supporting technical assistance for flood risk management studies (Baidoa, Beledweyne, and Dhusamereb) and a planned solid waste management pilot for Mogadishu. The Mission encouraged the PCU and PIUs to identify and advance proposals for additional technical assistance needs.

16. **Planned activities.** The government will identify additional technical assistance and analytics priorities under the project. This includes institutional strengthening on urban governance and roles and responsibilities of the three tiers government (FGS, FMS, and cities) on resilient urban infrastructure service delivery. Discussions on the best approach to stabilization in Dhusamareb and Beledweyne are ongoing. It was agreed during the mission that the PCU will commence procurement of the first phase of the stabilization assessment. The Terms of Reference (TOR) was discussed and agreed during the mission.

Component 3: Project Management and Capacity Building (US\$30.5 million)

17. **Progress to Date.** Key accomplishments include the development of a geo-referenced monitoring system and a web-based Management Information System (MIS), more structured coordination between the PCU and the PIUs, and the delivery of impact assessment reports for Baidoa, Garowe, and Kismayo that examine the impact of completed SURP-II works to host communities (See Annex 5 for the completed reports). A dedicated PCU M&E staff has been hired to institutionalize use of the MIS across the project and to support the migration of the MIS to be hosted directly by Government. The PCU and PIUs are fully mobilized.⁷ The project is in its third year of implementation and increasingly focusing on sustainability. 104 municipal and project staff were trained on topics ranging from Grievance Redress, E&S safeguards, Community Engagement and M&E. In August 2024, project and FMS MPWRH engineers joined a learning exchange with the Government of Sri Lanka to build capacity around implementing citywide drainage systems. The MPWRH is developing a whole-of-government capacity building plan to enhance technical skills and certification of government engineers. This TA will enhance municipal-led civil works, while also supporting higher levels of FGS/FMS engagement, supervision, and quality control. The mission agreed that the joint plan, including possible SURP-II and SHIIP support, would entail a phased approach that emphasizes hands-on-learning while leveraging existing learning and engagement from the UNOPS and successful PIUs.

Planned activities. The next Mayor's forum is planned for June 2025 (topic to be discussed), global exchanges on livable cities, amongst others. The Bank team is also engaging the Global Center on Adaptation to develop an Urban Climate Resilience Master Class. The project will continue providing trainings to municipal staff, in addition to PIUs, to take more active ownership of data management and quality control for the sustainable management of the MIS beyond the project. This will also include the roll-out of the government's capacity building plan, as well as capacity building plan for FGS and FMS on standard and policies for managing urban infrastructure. Annual contract management and procurement training, FM training, and ESF training, will be expanded to municipal staff and FMS.

Component 4: Response to Urban Forced Displacement (US\$65 million)

⁷ Ongoing staff recruitment includes a new Beledweyne Project Coordinator, M&E Specialist for BRA, and Community Engagement officers for Beledweyne and Dhusamereb. In addition, the Mission agreed to recruit an additional PCU Engineer to improve the efficiency of quality reviews.

18. **Progress to Date.** The US\$65 million project drought response (100% utilized) was activated for a two-year period and closed in September 2024.⁸ Key achievements include 452,148 people benefitted from health and nutrition services, of which 68% women and 77% IDPs. Cash assistance was provided to 163,054 beneficiaries, of which 86% women headed households and 100% IDPs. Around 300,000 people benefitted from temporary settlement, as part of housing, land, and property (HLP) intervention in Garowe, Baidoa, and Mogadishu, following drought in 2021-2022.

19. **Planned activities.** The government and IOM will focus on communicating project impacts and learning, including final reporting and closing ceremonies by December 2024. IOM has an 11-month defects and liabilities period which are contractually obligated, and further joint monitoring will continue to identify and address any issues.⁹ The project will register all relevant beneficiary information into the FGS universal beneficiary registry developed by MOLSA and supported by WFP under the Baxnaano program. This requires IOM to sign a data transfer agreement with MoLSA but pending a clear timeline and subsequent data transfer.

IV. FIDUCIARY COMPLIANCE

Procurement

20. **The procurement performance remains Moderately Satisfactory.** The mission noted positive progress in the implementation of procurement activities. Most of the procurement agreed actions from the previous mission have either been achieved or are at the advanced stage of completion. The aggregate total of the procurement activities since the project implementation period started is US\$ 237,249,731.39, of which US\$ 83,246,674.46 (35.10%) have been completed, US\$ 95,512,560.16 (40.25%) are on-going, US\$ 58,490,496.77 (24.65%) have been initiated and currently in various stages of procurement, and US\$25,987,226 (17.41%) have been planned but not initiated. The mission emphasized that the planned but not initiated activities should be expedited.

21. **Staffing.** The PCU also finalized the recruitment of the new Project Procurement Specialist, and the Consultant will be reporting in November 2024. Also, it was agreed during the mission that procurement activities not yet finalized/being planned should be expedited and that all contracts should be successfully executed before the project end date of December 31, 2026.

22. **Post review.** The mission was informed that since July 1, 2023, the prior review threshold applicable in accordance with the Bank procurement policy applies to this project except for

⁸Urban areas were experiencing a large inflow of internally displaced persons (IDPs) triggered by the 2021-2023 drought. Under the first AF, US\$20 million was allocated to the CERC (from component 1) to support a project drought response (the CERC was activated on July 19, 2022). The dedicated drought response component (Component 4) was introduced under the second AF and the funds from the CERC added to the new component. The project provided support on housing, land, and property (HLP) and basic services (water, sanitation, and hygiene [WASH] and/or health) in Mogadishu, Baidoa, and Garowe. The FGS engaged the International Organization for Migration (IOM) as an implementing partner through an output agreement signed in September 2022. IOM outsourced elements of the response to its Danwadaag Consortium comprised of international and local nongovernmental organizations (NGOs). Through US\$45 million of CRW-ERF financing, a 'minimum response package', including cash assistance, was introduced under the second AF (excluding additional investments in HLP). An amendment to the output agreement was signed between the FGS and IOM in April 2023 to scale implementation.

⁹ The shelter design for Baidoa was updated per the revised ESMP on January 22, 2024, including vendors constructing CGI shelter walls and roofs with 10% of the most vulnerable households receiving fully built concrete shelters, which was informed and endorsed through government and community consultations.

Beledweyne and Dhusamareeb Municipalities PIUs. In this regard, the World Bank will conduct the first post review of the activities not initially reviewed by the World Bank this FY.

23. **Mandatory use of the new Standard Form of Agreement (SFA).** Starting November 2024, it will be mandatory to use the new SFA dated July 2024 agreed between the World Bank and the United Nations Agencies. The template includes new Environmental and Social (E&S) provisions.

Contract Management

24. Contract Management is a key concern. Issues include delays in submission of payment request, mobilization delays/multiple contract amendments, unmet contract timelines, failure to follow Contract Management Plan among others. Proposed mitigation measures discussed/agreed on include improving Client/Contractors Contract management skills, expedited payments to contractors and strengthening proper planning during Contract implementation period. On capacity building, the Bank conducted a virtual procurement training in July 2024 and another training (face-to-face) on Contract Management was conducted in Nairobi from October 14 – 17, 2024. The PCU/PIUs staff attended the training. It was agreed during the mission that continuous procurement and contract management training are needed to improve project implementation.

Financial Management (FM)

25. **The financial management (FM) performance is Moderately Satisfactory**, and the FM risk is deemed Substantial. See Annex 2 for a Table of Disbursements as of November 6, 2024.

26. **Staffing.** The mission acknowledged strong and high capacity of PCU FM specialist for the project. As stated in the Financing Agreement, the project should maintain staffing of core PCU team, including FM specialist, throughout project implementation.

27. **Disbursement.** The level of disbursements at mid-term stood at 48%, which is considered moderately satisfactory. The cumulative budget absorption rate was also noted to be moderately satisfactory with significant commitments that are expected to boost the overall project expenditure. The risk of delayed accountability by the UN implementing partners was noted and the project requested to follow up on the submission of requisite financial reports from the UN agencies to facilitate accountability of UN advances in the Bank's client connection system. The mission also advised the project to monitor the foreign exchange losses between the SDR and USD and reorganize project activities accordingly.

28. **Submission of Interim Unaudited Financial Reports.** The project is up to date regarding submission of quarterly interim unaudited financial reports (IFR) to the World Bank including the latest IFR for the quarter ended June 30, 2024. The IFR for the quarter ended September 30, 2024, was submitted to the Bank by November 14, 2024. The latest FM supervision report highlighted inadequate internal audit oversight, delays in payment processing, gaps in accounting for advances to the Federal Member States and delayed deployment of the PCU Procurement Specialist. The external audit report for FY23 expressed an unqualified (clean) opinion on the financial statements but flagged gaps in internal audit oversight. The project was advised to address the issues noted in line with the agreed FM action plan.

V. ESF Compliance and Performance

29. **The overall E&S performance remains *Satisfactory*.** The project's E&S Risk Classification (ESRC) remains High (High in social and Substantial in environment ratings). Section VIII highlights the MTR and ISM Agreed Actions, including measures to strengthen the inclusion of women, youth and Persons with Disabilities (PWDs), captured under Annex 6.

30. **Implementation of Environmental and Social Commitment Plan (ESCP).** The implementation of ESCP is proceeding as planned despite the extreme FCV circumstances, including the limited presence of government institutions, significant physical insecurity, and the intensifying socio-economic impacts of climate change. The Bank commends the PCU/PIUs for making substantial progress in the management of E&S risks in the project. The mission was informed that the project resolved 99 out of 106 grievances reported since the last Mission in May 2024; secured funds to compensate displaced PAPS and, particularly in Mogadishu, where the PIU has deposited US\$ 400,000 to an escrow account; finalized the recruitment of E&S specialist for Kismayo and the Community Engagement Officer for Beledweyne to onboard on December 1, 2024, and January 2025 respectively; strengthened stakeholder engagement; promptly reported to the Bank, the fatality incident in Garowe and implemented all the corrective and preventive actions; included the requirement for contractor's to submit Local Recruitment Plans (LRPs) during bidding and issued land ownership documents to 1000 IDPs resettled in Hoodale settlement in Garowe. Despite these achievements, the PCU/PIUs need to continue the deliberate targeting of women, youth, and PWDs for employment, upskilling, and internships, and disaggregate data to include more categories of stakeholders reached, such as PWDs, minority clans, youth, older persons and other vulnerable or disadvantaged groups.

31. **Staffing.** The mission acknowledged strong and high capacity of PCU E&S specialist. The PCU/PIUs to build the capacity of SURP II staff, especially the Female Community Engagement Officers, e.g., through certification; undertake cross-city exchange learning and produce a documentary highlighting the SURP II success stories. The mission noted that in some cities, such as Baidoa, women have been trained and are actively involved in construction-related activities such as blocks interlocking; however, more efforts are still needed across the six cities. Hence, annex 6 captures an action plan discussed between the SURP II gender and GBV team, the Bank's E&S team, and contributions from the mayor of Beledweyne to strengthen inclusion efforts under the project. The plan focuses on upskilling, internships, contractor employment of skilled and unskilled locals, and engagement of PWDs in jobs they can do safely.

32. **Compliance to ESS.** The Bank advised the PCU/PIUs to ensure that the design of sub-projects such as roads and drainage system adhere to the safety provisions under ESS 4, such as providing appropriate and safe pedestrian access paths/routes and drainage tunnels.

33. **Baidoa shelters under Component 4.** The mission recommends for the PCU, PIU Baidoa, and IoM to proactively inspect the shelters in Baidoa to ensure any structural challenges are promptly addressed, to ensure that activities under the forced displacement component are concluded with no pending E&S obligations, including grievances.

VI. PROPOSED PROJECT RESTRUCTURING

34. **Proposed Project Restructuring and Additional Financing.** A restructuring and additional financing is proposed to: (i) revise project name; i.e. from Somalia to Somali (as Somaliland will be represented by Hargeisa city); (ii) revise the Results Framework (RF) to reflect additional activities and adjust selected indicators; (iii) add Hargeisa as a new city under the project;

(iv) extend project closing date to allow for investments in Hargeisa and to continue with investments in current participating cities; and (v) add capacity building for MPWRH FGS and FMS as part of Component 3. The Project Implementation Manual (PIM) will be updated following MTR discussions. This include updating roles and responsibilities of MPWRH FGS and FMS, and role of participating cities.

Summary of Proposed Restructuring

Proposed Changes	YES	NO
Program's Development Objective		X
Program Scope Note: to include Hargeisa	X	
Results Framework Note: to adjust for new activities and end target for selected indicators	X	
Legal Covenants		X
Loan Closing Date (s) Note: proposed 2 years extension to ensure completion of investments in Hargeisa and additional activities in current participating cities	X	
Additional Financing Proposed – pending official request letter to the Bank Note: (i) to add funds for Hargeisa – setting up PIU, FS/design, civil works; (ii) capacity building for FGS, FMS, and cities; and (iii) PCU/PIU project management cost	X	
Change to Financing Plan		X
Reallocation between and/or Components		X
Change in Key Parameters (Disbursement Arrangements) Note: add disbursement arrangement between FGS and Somaliland for Hargeisa	X	

35. **Proposed changes to the Results Framework indicators.** It was agreed during the MTR mission that a few indicators need revision, to ensure alignment with cities' priorities and ability to complete investments by project closing date, December 31, 2026. See Annex 1 for proposed RF changes.

VII. MTR AGREED ACTIONS

PCU			
1	Phased and joint capacity building proposal for government engineers	PCU SURP-II and PCU SHIIP	Proposal by Dec 10, '24
2	Recruitment of additional PCU engineer	PCU	Jan '25
3	Agree with IOM on the transfer of data and rectification of work in Baidoa during DLP period	PCU and IOM	Dec '24
4	Amendment of UNOPS TA contract (<i>to include Dhusamareeb and Beledweyne and extend time/inputs for other cities</i>)	PCU/PIUs/UNOPS	Jan '25
Baidoa			
1	Sign Package 3A and 3B contracts	PIU/PCU	Dec 31, '24
2	Prepare technical report on action required on Package 2 road drainage and walkways.	PIU/PCU/UNOPS	Nov 30, '24

3	Sign contract for design of Citywide drainage design and Northern Link Road	PIU/UNOPS	Nov 30, '24
Kismayo			
1	Submit revised program works and recovery plan for package 2A and 2B	PIU/UNOPS	Nov 29, '24
2	Sign package 3 contract	PIU/PCU	Nov 30, '24
3	Sign contract for citywide drainage FS and DED	PIU/PCU	Nov 30, '24
Garowe			
1	Prepare detailed designs for citywide drainage package 1	PIU/UNOPS	Dec 31, '24
2	Publish request for bids for urban roads Package 1 works	PIU/PCU	Jan 30, '25
3	Publish request for bids for trunk drainage Package 1 works	PIU/PCU	Jan 17, '25
4	Publish request for bids for PIU office building works.	PIU/PCU	Feb 7, '25
Mogadishu			
1	Publish request for bids for 4 packages of urban road works	PIU/PCU	Nov 29, '24
2	Issue variation order for cleaning of additional 2.5km of existing trunk drainage	PIU/PCU	Nov 29, '24
3	Prepare detailed designs for citywide drainage outfall O-5, O-16 and O-1	PIU/UNOPS	Mar 28, '25
4	Sign contract for 4 packages of urban roads	PIU/PCU	Feb 28, '25
Beledweyne			
1	Publish request for bids for Package 2 (Road #3)	PIU/PCU	Jan 5, '25
2	Sign contracts for Package 1B (Road #2)	PIU	Mar 22, '25
Dhusamareeb			
1	Publish request for bids for Package 2 (Main Road)	PIU/PCU	Jan 30, '25
2	Sign contract for Package 1 urban roads	PIU	Mar 29, '25
3	Publish request for bids for Public Park	PIU/PCU	Jan 24, '25
4	Prepare detailed designs for 1.5km Market Roads	PIU/UNOPS	Mar 15, '25

Annex 1. Proposed Changes to Results Framework Indicators

Current indicator	Proposed revision	Remarks
Urban roads rehabilitated or upgraded (Kilometers) Current value: 31.67 km	Revise target to 70 km	Following the third AF, the cities shift priorities towards drainage given increasing flood risks. The

Target: 90 km		end target may need to be adjusted to reflect the shift in priorities.
Pedestrian walkways constructed (Kilometers) Current value: 34.33 Target: 90	Decrease target to 70 km (in line with roads target)	This is to reflect revised number of km of roads rehabilitated or upgraded.
Number of person days of employment created (days, % female, % IDPs, % host) (Number) Current value: 206,398 (23% IDPs, 15% female) Target: 400,000	Introduce disaggregation for youth	Corporate scorecard indicator to include youth
Length of trunk drainage improved by the project Current status: 3 km Target: 22.4 km	Revise target to 15 km and revise name of indicator	Proposed revision to the indicator name to include all drainage work.
	Introduce new target on reduced flood risk, e.g. # of people benefitting from reduced flood risk or area of land with reduced flood risk	An additional target is needed to reflect the work undertaken that reduces flood risks in urban areas
Number of beneficiaries benefitting from cash assistance (number, % women, % IDPs) (Number) (Number) Current status: 163,054 (100% IDPs, 86% female) Target: 350,000	Decrease target to 163,000	While the number of households reached exceeded the target set in the output agreement with IOM, the number of individuals benefitting was less than estimated. This is due to average household size of registered IDP households (3) was significantly smaller than the average household size in Somalia (7 in urban areas).
Number of individuals treated with health and nutrition services (number, % women, % IDPs) (Number). (Number) Current status: 452,148 (68% women and girls, 77% IDPs) Target: 178,467	Increase target to 450,000	Target overachieved: (i) increased demand by the new IDP arrivals in Dayniile and Kahda districts. The Elnino floods resulted in widespread movement of people from flood-affected districts of lower shabelle to Banadir region; (ii) increased influx of IDPs and diseases outbreaks in Baidoa due to Elnino rains.
Number of individuals benefitting from WASH services and investments (number, % women, % IDPs) (Number). (Number) Current status: 315,337 Target: 330,000	Revise target to 315,000	This target should be revised, as it was set before the output agreement for the AF2 contract with IOM was finalized.
Number of beneficiaries of HLP services (number, % women, % IDPs) (Number). (Number) Current status: 129,211 (39% women, 100% IDPs) Target: 341,100	Decrease target to 129,000	This target should be revised as it exceeds end target agreed in the output agreements with IOM.

Annex 1A. Detailed Implementation Progress

1. Baidoa

Implementation progress. Baidoa has three contract packages as shown in the above table. Package one worth US\$3.98 million involves the construction of 3.9km¹⁰ roads with associated drainage and three box culverts, pedestrian walkways, and street lighting. DOCOL Construction and Logistics Company was awarded the contract on February 15, 2021, but the work did not start until August 2021. Initial delays were due to the Government's late payment of advance money, delays associated with the operationalization of the Security Management Plan (SMP), specifically agreement on the security costs, the contractor's delay in mobilizing key equipment¹¹ and contract management inefficiencies, and relocation of utilities at the six-cell box culvert and eight septic tanks on Road 1A. Despite the delays and a ten-month extension of contract period, the works were completed on March 31, 2023. Defects liability period (DLP) ended on March 30, 2024, thereafter the contractor rectified minor defects and was issued with a defect's liability certificate.

Package 2 contract was also awarded to DOCOL for US\$5.95 million over 18 months for the construction of three roads totalling 9.8km¹², including drainage, pedestrian walkways, one bridge walkway, and streetlights. Due to RAP issues, Hanano road was rerouted which increased the length by 1Km. Also, a section of road 6 (package 1) was damaged following heavy rains in September - December 2024. These variations increased the cost of package 2 by US\$1.31 million and revised the contract price to US\$7.26million. UNOPS provided a climate resilient design for that included a rigid concrete pavement which the contractor implemented. The mission noted that since the last mission in May the Contractor has mobilized more resources such that works were not on schedule at 98% completion. Significant delays had been caused by lack of some key equipment, heavy rainfall and exacerbated by delayed payments to the contractor. Asphalt works were completed on all roads while construction of drainage, footpaths and road furniture was progressing well. However, the mission noted with concern that (i) drainage was missing in several road sections, (ii) streetlighting was not provided for all three roads, (iii) gaps on footpaths along Road 1B were risky as pedestrians could get injured, (iv) access culverts to properties were not sufficient, and (v) in some sections of Road 5, the embankment is high above the properties with slopes not protected and drainage not provided. The mission also noted the rapid urbanization of the area around Hanano road, which at the time of design in 2019 was considered peri urban. This has created the need for improved road drainage and junction geometry design and provision of streetlighting. UNOPS reported that except for drainage works on Road 5 that connect to Road 2, the other activities valued at US\$150,000¹³ can be done within 3 months during the defect's notification period, since the contract end date is November 18, 2024, alternatively contract to be extended by three months. UNOPS team, and PCU engineer visited Baidoa on Sunday, November 10, 2024, and together with the PIU team, inspect these works, assess the gaps, and prepare a technical report on what is feasible under the current contract and what could be done under Package 3. The mission reiterated that further extension of time on this contract will not be acceptable.

The last package was divided into two contracts. PCU was reviewing the bids for Package 3B¹⁴, the contract is expected to be signed by November 30, 2024, and works to commence by January 2025. PIU was evaluating bids for Package 3A for 2.47km Baidoa main road, and the works are expected to commence in February 2025. The two packages include outfall drainage that will reduce flooding. The mission noted a slippage of 2 months in the commencement of the works and requested Baidoa to expedite the procurement.

¹⁰ Road 6 – Ali Amhar Road (2.8km) and Road 1A - Hospital Road (1.1km)

¹¹ Road transportation of equipment is not possible due to insecurity and the Contractor experienced challenges in airlifting heavy equipment from Mogadishu. Two excavators were required for earthworks, but only one was available in March 2022, 7 months after the contract start date.

¹² Road 5 - 30KA road (3.2km), Road 7 - Hannano 2 Road (3.9km) and Road 1B - Hospital Road (2.7km)

¹³ About US\$800,000 is unutilized and available for these works under the contract.

¹⁴ Package 3B involves construction of 1.2km Sharif Gacamey Road, 1.5Km Unaye Road, and 1.38Km Murasal Road.

Technical Studies. Citywide drainage and the Northern link road have been identified as priority investments under AF3. The TORs have been reviewed and cleared by the Bank and, no objection to single-source UNOPS granted. However, the signing of the contract was delayed since UNOPS did not initially use the new output contract template. The Bank has now cleared the draft contract for signing. The timeline for the designs for the 9km gravel road and citywide drainage are currently being determined.

ESF. The Mission noted significant challenges with universal access on some roads. The contractor had substantially completed the roads without making provisions for some residents to access their houses. The footage shared by the PIU also showed some sidewalks that had gaps in between them, ostensibly for stormwater drainage off the pavement, but which pose hazards to pedestrians. The PIU was urged to urgently address both matters to forestall any incidents affecting homeowners, pedestrians and the larger public. The Mission was also informed that, following the incidents involving roofs being blown in the Barwaaqo IDP settlement site, IOM had agreed to address the issue with the contractor on the site and ensure that no harm befalls the residents of the site, who are going to inhabit the houses. The team was advised to ensure that an assessment was done to review the fitness for human habitation of the shelters under construction urgently and to put the matter to rest. The Mission agreed to a recommendation for PCU and PIU engineers to jointly carry out site safety inspections after the remedial works are completed.

Key issues as reported by the Baidoa PIU include the following:

- **Security risk management:** The PIU reported no project-related security incidents at the time of the mission. The PIU confirmed police presence at project sites and that police officers had received orientation and signed Codes of Conduct.
- **Environment, Occupational Health and Safety (OHS)/community health and safety:** The Mission observed that there was improved use of Personal Protection Equipment (PPE) by workers, as the contractor has been consistently implementing a “No PPE, No Work” policy. To enhance the safety of road users, the Mission had recommended the installation of permanent road safety signage, but this has not been implemented across all the roads. The Mission continues to encourage the PIU to replace stolen or damaged road signs, erect speed bumps, and enforce compliance by road users, especially by working even more closely with the municipal government. The Mission particularly **recommended** closer engagement with the local police to enforce traffic management as well as increasing community awareness on Child Labour and GBV issues.

2. Kismayo

Implementation progress. Kismayo has three contract packages as shown in table above. For package 1, the PIU contracted the Chongqing Overseas Construction Corporation (COCC) on May 24, 2021, to construct 7.75km roads and a drainage outfall for US\$5.4 million.¹⁵ However, physical work only began in February 2022 after an eight-month delay due to the contractor’s challenges in mobilizing equipment and personnel and due to cash flow challenges throughout the life of the works. That led to a shortage of materials on site, delays in equipment repair, and temporary work stoppages due to a strike by unpaid workers. As a result, the COCC contracted two local subcontractors to help finalize the remaining works. After three contract extensions, extending the project end date to December 31, 2023 (from 18 to 31 months), the contractor finally completed the work on December 31, 2023. The contractor completed minor outstanding works and is addressing minor defects during the 12-month defects liability period (DLP).

¹⁵ This was above the estimated by US\$500,000 and pulled from Package 2.

Package 2A was awarded to Kulmiye General Services Limited on October 15, 2023, to construct 4.7km of roads for US\$4.1 million, and works commenced on January 18, 2024. The mission noted the delay in completion of the works that are to be completed on December 31, 2024, with 65.1% actual progress to date. The contractor will request a three-month extension of time, revise the program of works, and prepare a recovery plan to ensure completion of work by March 31, 2024.

After experiencing delays in procurement when the bidder with the most advantageous bid declined to sign the contract, Package 2B was awarded to Kulmiye General Services Limited, the next ranked bidder, on May 1, 2024. The mission noted with concern slippage in the program of works with 8.5% progress to date. This was due to lack of key equipment for the works and instances of delayed payments. Whilst the contractor was able to mobilize equipment for each contract, the main equipment for package 2B was in use in package 2A, which has contributed to the slow progress. Kismayo assured the mission that since package 2A earthworks had been completed, all equipment would now be dedicated to package 2B. Package 2b Works will take 14 months, ending July 31, 2024. The Contractor will submit a recovery plan and updated program of work.

Procurement of Package 3 works¹⁶ is at an advanced stage, with contract signing expected by November 15, 2024. The contract's duration is 16 months, with the planned completion date in June 2026.

Technical studies. The citywide urban flood risk and stormwater drainage assessment (FRA) in February 2023 identified priority areas for drainage upgrading and flood risk management in Kismayo. The TA, financed by Global Facility for Disaster Risk and Recovery (GFDRR), was implemented by Hydronova. The pre-feasibility report provides a mix of grey and green infrastructure, which is primarily made of concrete and steel pipes and channels, and nature-based solutions to attenuate the stormwater in the city. The proposed measures are set out in six investment packages totaling US\$230 million, with the priority package of US\$44 million. To advance the FRA to a feasibility study and detailed engineering design, Kismayo expects to sign the consultancy contract in November 2024, and the assignment will take 10 months. However, there is no funding for the investments to be designed, but this creates an opportunity for Kismayo to approach other donors to support addressing these most needed investments.

To ensure local ponding does not occur on SURP II roads, Kismayo with support from UNOPS under the TA is preparing designs and bidding documents for three outfalls¹⁷ of length 1.93km and two detention ponds in line with the citywide drainage pre-feasibility study. These have been identified for investment, as the Municipality undertakes Kismayo city-wide drainage feasibility study and engineering design. Preferably, this detailed study should precede the drainage investments. However, it is stated that the proposed investments are “no regret” type interventions that will not interfere with investments that may be proposed under the citywide assessment. At the upstream end of the outfalls are retention ponds that too are identified for improvement as green public spaces. Introduction of regulation gates for ponds may be considered to drain water prior to storm events, to increase retention. Kismayo proposes to implement these as variation order under the ongoing road contracts.

ESF. All subproject-specific E&S instruments for Kismayo for packages 1 and 2 are under implementation. The PIU has updated the E&S instruments for package 1 to reflect package 2 and the newly designed Argo drainage outfall and the instruments have been disclosed in-country. The sub- contractors are implementing the sub-projects C-ESMP, LMP, and SMP and all newly recruited workers/staff have signed the codes of conduct.

¹⁶ Package 3 included 1.71km of Road 2a, 1.3km of Road 4B, and 2.1 Road 10.

¹⁷ Three outfalls are 840m Olympic, 740 Majengo, and 350 Old Stadium outfalls

Key E&S issues reported by the Kismayo PIU include the following:

- **Drainage outfall proposed.** There are new issues arising around the newly proposed drainage outfall for Kismayo, including possible impact on biodiversity, as well as the stormwater retention ponds. The PIU has updated and disclosed sub-project-specific E&S instruments for Package 1 to reflect Package 2 roads, and the newly proposed drainage line through Argo Junction. **Security risk management:** An MoU was signed between the COCC, the contractor, and Kismayo police commissioner on April 25, 2022. The PIU in Kismayo was confident about the overall security prospects, noting that the recent terror attack, which took place very close to the project site in October 2022, was not aimed at the PIU offices nor the project. Regardless, the PIU must remain vigilant and follow strict mitigation measures outlined in the SMP.
- **Environment, OHS/community health, and safety:** The Mission recommended that **the PIU** review data from the contractor report to establish data gaps. The Mission noted that it was the responsibility of the E&S specialists in all the PIUs as well as at the PCU, to flag out where there are data gaps and follow it up with the contractors.

3. Garowe

Implementation progress. Garowe has two investment packages financed under SURP-II as shown in the above table. Package 1 includes the construction of four urban roads totaling 6.3km¹⁸, side drainage, streetlighting and walkways. The contract was signed with TTN Construction on April 18, 2021, for of US\$3.73 million. Package 1 civil works were completed and handed over to the Municipality on November 1, 2022, one month before the contract end date of November 30, 2022. The municipality has also planted 500 trees along the Package 1 roads. The contract realized savings amounting to \$638,719 that was used to carry out additional works under variation order 1 – streetlighting (297 lights), extension of Wadajir road (460m), and drainage outfalls along Tawfiq road and Indija road (930m). To complete these additional works, the completion date was extended to May 31, 2023. All the additional works were completed in time.

The Package 2 contract was also signed with TTN on April 3, 2022, and includes Gambol Road (1.22km) and Gambol Bridge (0.14km), at US\$3.86 million. Initial delays in starting physical works occurred due to the need for review and verification of bridge design by an independent third party. However, the construction of the road section started in February 2023 and is 98% complete. As the review of the bridge design was going on, the Contractor submitted a Value Engineering Design (VED) for the bridge. The design review consultant completed the review of the original design and the contractor's VED in July 2023 and recommended the VED. The commencement of bridge works was further delayed due to lengthy negotiations on the VED cost estimate. Design changes and increased scope resulted in increase in cost by US\$2.45 million. After lengthy negotiations with the Contractor, Garowe finally signed the variation order and addendum to the contract, paving the way for the bridge works to commence in December 2023. UNOPS TA has recruited an experienced bridge engineer to supervise the bridge construction. Whilst hoped to complete the works a few weeks ahead of scheduled completion date of December 3, 2024, an incident that resulted in a fatality on site caused a stoppage of work for 3 weeks. The bridge works are still on schedule with progress at 95%. A saving of US\$817,000 has been realized, and Garowe intends to improve traffic flow along the Garowe main road by constructing 0.7km of East Africa Road and 0.5km of Garowe main road junction improvement. To complete the new works, the contract period will be extended by 2 months to January 31, 2025. The mission visited Garowe on November 10, 2024.

¹⁸ 2.02km of 30th Street, 0.7km of Injida Road, 2.15km of Towfiq Road, and 1.44 of Wadajir Road

Technical Studies. Design of citywide drainage investment to be partly funded under AF3 is underway. In December 2023, Garowe contracted UNOPS to design priority drainage investments that were identified under the urban flood risk assessment/pre-feasibility undertaken by Hydronova in 2023, to alleviate the impacts of frequent flooding. However, UNOPS did not commence work until late March 2024 due to delays in the disbursement of funds from the government. The pre-feasibility presented options and priority investment/packages, a total of US\$247 million in FRM investment needs. Preliminary design estimates for investments in six priority urban zones selected for detailed engineering designs is US\$68million. However, under SURP II Garowe has available US\$ 4 million, which is not sufficient for stormwater drainage in one zone. Detailed engineering design for the first package will be ready in December 2024, the remaining 5 packages will be ready by February 2025. The prepared investments create an opportunity for other donors to support Garowe in addressing the flooding challenge in the city.

Designs for Garowe urban roads and municipality building are progressing well. Designs for the 20km of roads are expected in December 2024. Preliminary estimates indicate that about US\$15million is required for the designed roads, but currently, Garowe has funds for 2Km only.

Assessment of the structural integrity and safety of the stalled municipality building for the PIU was completed with positive recommendations. The architectural and engineering designs for the completion of the building will be prepared and will address gaps identified in the assessment report. The bidding documents will be ready in December 2024.

Key E&S issues reported by the Garowe PIU include the following:

- **Security risk management:** Four police officers, one of them female, have been deployed to Package 1 sites. In August 2023, Garowe Municipality deployed armed police officers to the Hoodale site following disruptions of civil works. The incident has been resolved and there are ongoing discussions for the Municipality to put up a permanent police post. No additional insecurity incidents and/or risks were recorded at the time of the mission.
- **Environment, OHS/community health and safety:** The PIU has planted several *Ficus Benjamina* trees on the road median. The Mission encouraged the PIU to closely monitor the growth of the trees and any unforeseen impact, especially on the pavement and community safety, as the species is particularly susceptible to heavy gales and winds. The Mission reiterated the previous recommendation that the newly completed roads should have EHS, and road traffic safety warnings and signposts erected prominently and painted on the main carriageway in thermoplastic quality to aid road users.

4. Mogadishu

Milestone	Quick Wins	PIU Office	Cleaning 6.7Km of existing drainage
-----------	------------	------------	-------------------------------------

Investments	4 catchment ponds dewatering and desilting and fencing (\$594k, Jan. 31, '23)	Construction of PIU Office	Cleaning and condition assessment of 5Km existing drainage
	2 community road (B10 and B20) drainage extension (\$393k, Mar. 31, '23)		
	- Cleaning and condition assessment of 700m existing trunk drainage. 1 community road (B15 Ceymiska Rd) construction (\$200k, Apr. 15, '23)		
Contract amount	US\$1.66 million	US\$560,481.00	US\$348,570.00
Current progress	Desilting of all 4 catchment ponds, B10 road drainage condition assessment, and construction of B15 (Ceymiska Rd) and B20 drainage extension all completed	19% (on schedule)	15% (on schedule, 2.42Km cleaned)
Contractor	Various	Alool Construction and Consultants	Target General Services LTD
Contract signing	Various dates	13th July 2024	27th August 2024
Commencement of works (Planned)	Oct. 2022	August 14, 2024	September 15, 2024
Commencement of works (Actual)	March 22, 2022	August 14, 2024	September 15, 2024
Completion of works (Planned)	June 22, 2023	August 14, 2025	September 14, 2025
Completion of works (Revised)	Oct – Nov 2023	TBD	September 14, 2025

Implementation progress. Implementation of civil works in Mogadishu is significantly delayed with minor quick disbursing investments undertaken so far, as Mogadishu's priority investments changed from urban and community roads to trunk drainage that has not been designed. BRA has now prioritized a mix of several quick wins and large-scale investments of four trunk drainage lines based on the Mogadishu citywide drainage master plan that the Bank funded. The eight quick wins shown on the above table have been completed. Drainage-related quick win activities have improved stormwater management in some parts of the city and public safety due to the fencing of the ponds. PIU office work commenced in August and is proceeding well on schedule. Cleaning of existing trunk drainage is ongoing, and 2.4Km of trunk mains in good condition have been identified so far. With the discovery of this trunk drainage network, it was agreed that BRA and the contractor find ways of enhancing the rate of progress to complete the identification of manholes, take invert levels, and alignment verification by November 15 so that the existing trunk drainage can be including in the citywide drainage modeling. It was also agreed that BRA will issue a variation order to include 2.5km trunk drainage lines not in the contract. Procurement of desilting of Sigale pond will commence once ES documentation is ready in December 2024, a slippage of 6 months from earlier planned dat.

Solid Waste Management (SWM) pilot. It was agreed during the mission that the Bank will invite a SWM expert to review the proposed activities for SWM pilot in Mogadishu. This will be further discussed with the MPWRH, PCU, BRA Mogadishu, and the Bank in November 2024.

Technical Studies: To advance the Trunk drainage masterplan prepared in 2018 (see Annex 1D) and delivered by UNOPS, BRA has commenced feasibility studies and detailed engineering design for Mogadishu city in July 2024. BRA experienced a delay in engaging design consultants when the competitive process was unsuccessful, leading to the single sourcing of UNOPS in December 2023 to undertake the designs. The trunk drainage lines are expected to have a transformational impact on urban flood management but will require a longer time to implement and are slow to disburse. During the mission, BRA shared with the Bank the feasibility study (FS) report, the Bank will review this by November 15, 2024. The FS prioritized three quick win (QW) trunk drainage packages, O-5 (1.44km), O-16B (13.7 km), and O-1(12.4km). The alignment of these trunk lines agrees with the masterplan thought with longer micro tunnel sections and higher cost estimates. BRA is also locating the existing trunk drainage lines, assessing their condition and taking technical survey and pipe profile information. Some discovered lines are as large as 2m diameter and in good condition. Due to the discovery of existing trunk drainage along O-2 and O-3, these two investments are no longer high priority and will be delayed. It was agreed to incorporate the existing trunk lines in the citywide drainage hydraulic modeling. Further, to expedite these investments, BRA will begin with outfall sections without micro tunnel, these include 1.44m on O-5, 3km on O-16B, and 4km on O-1 towards the ocean. UNOPS will complete preliminary engineering design in December and detailed engineering design in March 2025 for all three priority trunk drainage packages together with the Mogadishu Airport trunk drainage package. ESIA will be ready in December 2024 and detailed topographic survey and geotechnical investigation ongoing. Designs for the other trunk lines will be undertaken thereafter and completed by mid 2025.

BRA has also prepared designs for nine urban roads, 13.1km delivered by UNOPS. The investment is in four packages estimated at US\$ 17.8 million.¹⁹

Key E&S issues reported by the Mogadishu PIU include the following:

- **Quick Win investments:** The approved E&S instruments were disclosed, with summaries of translated copies in Somali of the approved instruments (ESMP and SEP, as well as the LMP) publicly disclosed on the BRA website and made physically available in the five target districts. The Mission was updated on the planned fencing of the rehabilitated ponds. The Mission recommended that the PIU conducts further discussions on geomembrane liners needed for Hilaac urban stormwater retention pond as they help in reducing groundwater pollution risks while also ensuring longer residence time of water, which results in community benefits. Further, E&S instruments will be updated to capture the Sigale catchment pond and the eight (8) urban roads.
- **Trunk Drainage:** To inform the selection and design of priority drainage lines, the E&S assessment will be conducted together with the Feasibility Study and the DED. The revised TOR has already been cleared by the Bank. The Mission advised the PIU/PCU safeguards specialists and engineers to closely collaborate in this process. While O-2 is a reasonably structured outlet and located in the safely protected port, O-16 is a smaller pipe discharging to the beach surrounded by business activities, busy roads and an illegal dump site. This discharge into a populated area may cause significant public health problems. The Mission and the PIU/PCU agreed on the need to carefully assess the resettlement impact (economic impact from drainage lines work) among others and consider alternatives in the forthcoming feasibility study and the ESIA.

¹⁹ P1 has one road 2km dual carriageway, US\$4.95m; P2 has two roads 4km, US\$4.95m; P3 has three roads 3.94km, US\$4.2m; P4 has one road 2.9km, US\$3.7m

- **Security Risk Management:** No project-related security incidents were recorded at the time of the mission.

5. Dhusamareeb

Milestone	PIU Office	Package 1	Package 2
Investments	Construction of PIU office and Laboratory	1 road (3.3km), side drainage, walkways, streetlights	1 road (4.9km) side drainage, walkways, streetlights
Initial Contract amount	0.419	Estimate - US\$5 million	Estimate - US\$4.9 million
Revised Contract amount	N/A	N/A	N/A
Current progress	80%	Published	Bidding docs preparation
Contractor	Somtech Engineering & Construction	N/A	N/A
Contract signing	Feb. 29, '24	Feb. '24	Apr. 3, 2022
Commencement of works (Planned)	Apr. 1, '24	Jan. 2024	Mar. 2025
Commencement of works (Actual)	Apr. 1, '24	N/A	N/A
Completion of works (Planned)	Sep. 30, '24	N/A	N/A
Completion of works (Revised)	Dec. 31, '24	N/A	N/A

Implementation progress. Construction of the PIU office and laboratory building is progressing well at 80% completion. The works were awarded to Somtech Engineering & Construction at US\$0.49 million and commenced in April 2024 and will be completed on December 31, 2024. Procurement of equipment for the materials testing laboratory will be delivered in December 2024. UNOPS has delivered engineering designs and bidding documents in two quick win (QW) packages for two roads (see above table). Package 1 has been published, and bids will be opened on November 21, 2024. The mission advised Dhusamareeb not to wait until package 1 commences to publish package 2, but to publish as soon as the bidding documents have been cleared by PCU since time is of the essence as project closes in December 2026. Commencement of civil works is expected in February 2025 for QW package 1 and April 2025 for QW package 2. These will be the first urban roads to be financed by the Bank in Dhusamareeb. UNOPS informed the mission that there are road contractors with the capacity to undertake the works, and it was possible to transport equipment and construction materials from Mogadishu and other major cities in Somalia. For the supervision of these works, the UNOPS TA contract with BRA that includes other four cities will be amended in December 2024 to include Dhusamareeb. Design for the 3,500m² public park was being reviewed to include more green spaces, while the design for 1.5Km market roads will be completed in February 2025.

6. Beledweyne

Milestone	PIU Office	Package 1B (Rd#2)	Package 2 (Rd#1)	Package 3 (Rd#3)
Investments	Construction of PIU office and Laboratory	1 road (3km), side drainage, walkways, streetlights	1 road (3.25km) side drainage, walkways, streetlights	1 road (3km) side drainage, walkways, streetlights
Initial Contract amount	636,826.48	Estimate - US\$4.35 million	Estimate - US\$3.8 million	Estimate - US\$2.87 million
Revised Contract amount	N/A	N/A	N/A	N/A
Current progress	13.5%	N/A	N/A	N/A
Contractor	Timely Transportation & Logistics Co.	N/A	N/A	N/A
Contract signing	Aug. 25, '24	N/A	N/A	N/A
Commencement of works (Planned)	Oct. 10, '24	Mar. '25	May '25	May '25
Commencement of works (Actual)	Oct. 10, '24	N/A	N/A	N/A
Completion of works (Planned)	Sep. 10, '25	N/A	N/A	N/A
Completion of works (Revised)	N/A	N/A	N/A	N/A

Implementation progress. Construction of the PIU office and laboratory building is on schedule at 13.5 % completion. The works were awarded to Timely Transportation & Logistics Company at US\$0.64 million, works commenced in August 2024, and will be completed on September 30, 2024. UNOPS has delivered designs and bidding documents in three quick win (QW) packages for three roads (see above table). All are under review by PIU and PCU to check that the designs are resilient to climate, especially flooding due to the location of the city along River Shebelle. Package 1B will be published in November. Subsequently, package 2 and 3 will be published. Commencement of civil works is expected in March 2025 for QW package 1B and May 2025 for QW package 2 and 3. These will be the first urban roads to be financed by the Bank in Beledweyne. UNOPS informed the mission that there are road contractors with the capacity to undertake the works, and it was possible to transport equipment and construction materials from Mogadishu and other major cities in Somalia. For the supervision of these works, the UNOPS TA contract with BRA that includes other four cities will be amended in December 2024 to include Beledweyne.

Dhusmareeb and Beledweyne Technical Studies. The institutional and urban infrastructure needs assessments were completed for both cities in early 2023. The PIUs contracted UNOPS in December 2023 to prepare feasibility studies, detailed engineering designs, and bidding documents for priority investments²⁰, including roads/drainage, bridges, and public parks, with civil works anticipated to start by

²⁰ Includes: (i) Dhusmareeb -- 10 sections of roads (approximately 24km) including drainage and solar streetlights; improvement of central market roads (approximately 1.5km); and development of a public park (3,500m²), and (ii) Beledweyne – 8 roads (22 km) and two bridges (120 m).

March 2025.²¹ Dhusamareb and Beledweyne PIUs simultaneously procured and are jointly undertaking a city-wide flood risk assessment to identify options for drainage upgrading and flood risk management and identify prioritized investments to pre-feasibility stage (similar to the studies that were conducted in Garowe and Kismayo), but detailed engineering designs will not be prepared as no funding for these investments is currently available. The consultants prepared an inception report and commenced the flood risk assessment study. In addition, UNOPS is preparing a feasibility study and detailed engineering designs for two bridges in Beledweyne. Two earlier identified sites have been dropped due to lack of access to the sites and new sites identified. The first bridge will be in a newly identified location where the farmers are willing to sell land for access road, while the second bridge will replace the current Liiqliqato Bailey bridge within the city. Community consultations, preparation of ESIA and technical investigations and surveys are ongoing. UNOPS indicated they will submit a workplan with new timelines for preparation of bridge design as changing the bridge locations midway into the assignment will have a significant impact on the delivery timeline and cost of the assignment.

Component 4: Response to Urban Forced Displacement

Implementation Progress. To date, US\$50.5 million has been disbursed to IOM, which has expensed US\$22 million and committed US\$22.3 million, or 68% of the total component allocation of US\$65 million. The component reached nearly 300,000 (81% of 371,000 targets of drought induced IDPs in Mogadishu, Baidoa, and Garowe as well as host communities. A third amendment to the output agreement was signed between the FGS and IOM 2023.²² To date, 2,450 latrines and 6 boreholes were constructed, and 2 health centers rehabilitated and equipped, and 106,450 individuals treated with emergency health and nutrition services, 23,860 women supported with ANC and PNC services, 9,357 children treated for early stages of malnutrition, 638 incremental housing units constructed, and 84,267 persons received lease agreements. The relocation commencement for Hoodal and Barwaaqo is approaching with Hoodal relocation expected to start during the week of May 19th, and Barwaaqo during the week of June 15th. Health operations in Baidoa and Mogadishu have received greater than expected coverage largely due to new IDP arrivals in Banadir IDP sites. Social service investments such as community centers, recreational equipment, tree planting/greening and health support have been scaled up in relocation settlements aimed at raising the quality of life within such communities. Delays with shelter procurement and shelter construction activities in Baidoa have pushed back the expected completion dates for shelter activities for Barwaaqo, requiring a conversation around extending timeframes for activity deliverables in Baidoa.

To date, 750 latrines and 2 boreholes were constructed, and 39,953 households received shelter and hygiene kits, 39,685 households received multi-purpose cash assistance (MPCA) (2 of 4 batches), 216,315 women and children received health and nutrition services, 21 health facilities supported to provide 10,647 children affected by moderate acute malnutrition and pregnant and lactating women, 21,468 children affected by severe acute malnutrition, amongst other support. Key challenges include delays in de-duplication for MPCA with WFP, delays in securing land tenure documents required for latrine construction, and additional health and nutrition needs related to late 2023 flooding.

²¹ Current timeline for key deliverables: (i) feasibility report, detailed designs, and bidding documents for quick wins 1 [November 30, 2024], (ii) feasibility report, detailed designs, and bidding documents for quick wins 2 [December/January 30, 2024], (iii) feasibility study and detailed designs for 2 bridges [March 30, 2025], (iv) award of road construction contracts for quick wins 1 [January 30, 2025], and quick wins 2 [February/March 28, 2025] and award of bridge construction contracts [September 1, 2025], however AF3 funds may not be adequate to finance all priority investments in Beledweyne and Dhusamareb.

²² To extend the project closing date to September 30, 2024, and decrease the commitment threshold to 60% (from 70) to release payments.

Annex 1B: Technical Note on Drainage Investment in Mogadishu

Drainage Investments- Overall

A Multi Criteria Analysis had been carried out to identify priority investment of the project that mainly resulted in the identification of selected roads, bridges and drainage investments in the project cities. In preparation for drainage investments; the PIU had carried out the necessary feasibility studies, preliminary designs, environmental and social impact assessments, detailed engineering designs and bidding documents; and these activities remain at various stages of implementation.

The Project Coordination Unit (PCU) had provided observations and recommendation in terms of important considerations for modelling and detailed design of these infrastructure investments. It is expected that these observations and recommendation are deliberated by UNOPS and associated design teams prior to finalization of the detailed designs; notwithstanding, the final design responsibility rest with the UNOPS and necessary technical rigor is expected. It is important to restore existing drainage systems to the extent possible as a way of initial alleviation of flooding. Once restored, an effective plan of action is to be deployed for continued regular maintenance.

The Municipalities must endeavor to preserve flood detention and retention areas as much as feasible and maintain the natural drainage paths. Secondary to flood reduction, they form important public spaces for recreation and greening the surroundings.


Implementation of most drainage packages will commence between March and July 2025; with an effective construction period of between 18-24 months. Once contract works commence, given the limited contractor capacity and complex nature of drainage engineering; the PCU/PIUs are advised to monitor progress diligently in close collaboration with UNOPS. With the asphaltting of previously gravel earth roads, increase in road foundation height and the introduction of new roadside drainage, increase of runoff is expected that could lead to local level ponding. It is therefore important that adequate cross culverts and leader drains are incorporated in the road design to prevent increased local flooding.

Drainage Investments in Mogadishu

The Master Plan for the Trunk Drainage in Mogadishu had been completed. After much deliberation, the flood infrastructure is proposed to be designed to accommodate a 25-year return period rainfall. The trunk drainage infrastructure required to drain such a storm consists of trunk mains of 4m diameter. The proposed construction methods for these include open cut sections of depth up to 8m and micro tunnelling. The expected cost of the trunk drainage network is USD 446 Million. The practicality of constructing drainage mains of 4m diameter using the construction methods proposed in a highly dense city; and the economic viability of the works proposed is to be further verified. Additionally, it was noted with concern that the existing drainage network in the city had not been included in the model; in effect ignoring its functionality. However, the BRA is undertaking a condition assessment of 6.7kms of the estimated 9.0km of the existing system network; and this work is to be expanded to cover the full 9.0km system. This report with the cross-sections, invert levels, manhole shaft locations etc. is to be shared with UNOPS by November 15, 2024, for inclusion in the modelling. The PCU/ PIU requested that modeling for return period of 15 and 10 years be done for informed decision making as with regards to return period to be used in the detailed engineering design.

Three “quick win” packages at a cost of US\$ 102 Million were identified from three (catchments O-5, O-16 and O1) of the seven trunk drainage catchment areas and were reviewed and approved by PIU. The figure below shows the Masterplan recommended Option 2 catchment areas and trunk drainage lines;

confirmed by the recently completed feasibility study. Catchment areas boundaries are marked in white, micro-tunnelling (trenchless technology) sections in green, and open cut trench sections in black. The ESIA and the detailed topographic survey and geotechnical investigation are ongoing. A decision is to be taken as to proceed with the design of these “quick wins” concentrating on their completion by end of December 2024 or to wait until the completion of the full study and designs by March/April 2025. The latter option would take 3-4 months longer but is the more prudent option to allow time to include the existing drainage in the model and as all analytics would be completed by then.

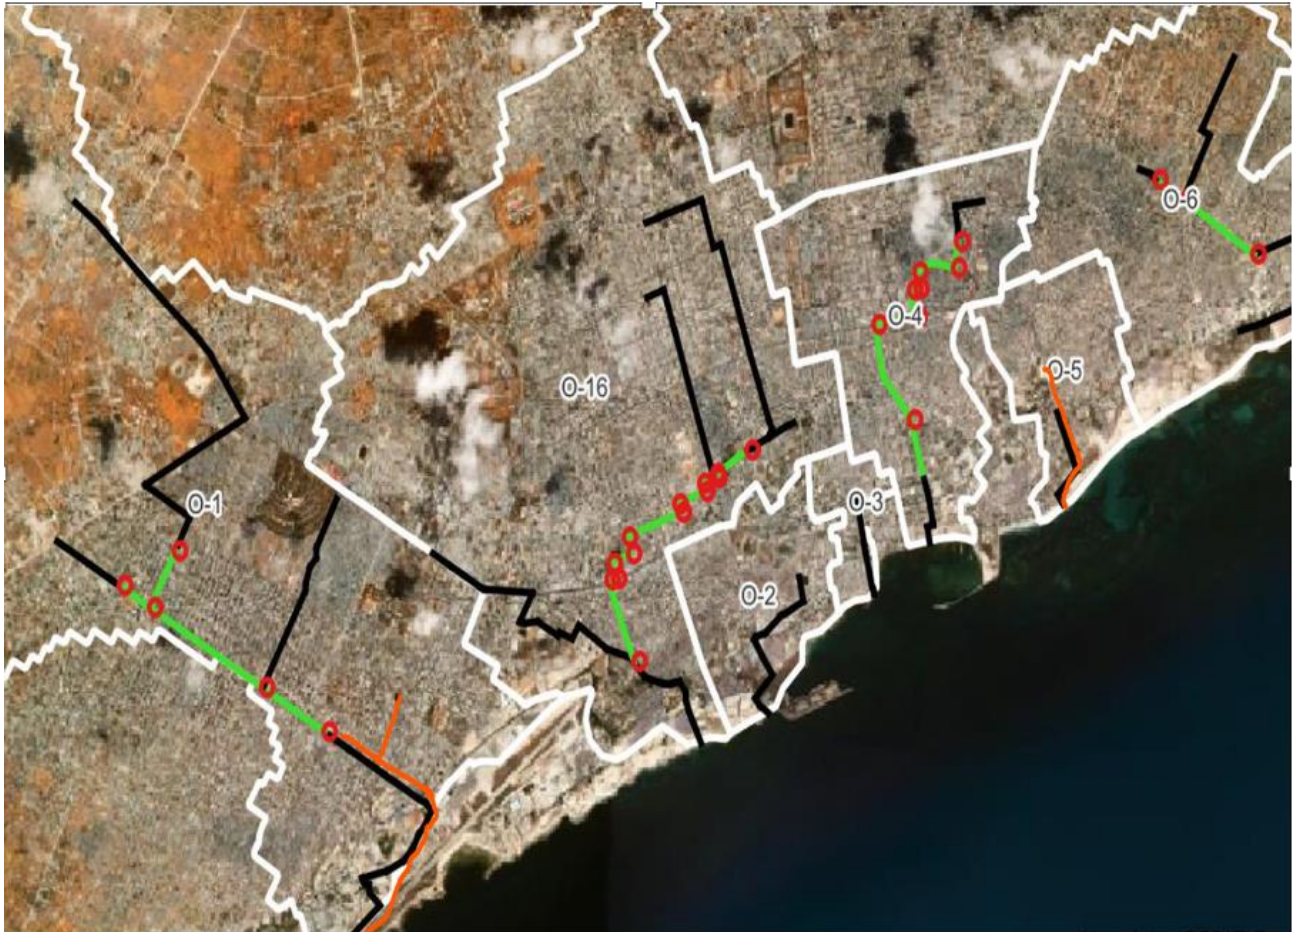

Map of Mogadishu Trunk Drainage Lines (Masterplan Preferred Option 2)

The detailed engineering designs for trunk drainage are expected to be completed March 2025. With the necessary review and approvals, bid document preparation and international tender processes, evaluation and award; some proportion of the planned works may not be undertaken within the current project period. Therefore, the Mogadishu PIU is advised to fully restore and rehabilitate the existing drainage network to the extent feasible and explore the possibility of carrying out some local level improvement to alleviate flooding in the shorter term.

It was also reported that the calibration of the model had been difficult due to lack of locally observed data. However, the model is aligned with the observations of the Master Plan of 2018 and therefore, the model calibration is within tolerable accuracy. In consideration of infrastructure investment proposed; the PIU in consultation with BRA Public Works Department and UNOPS is advised to consider setting up a limited number of rain gauges and streamflow measuring instruments to facilitate more accurate model calibration.

Annex 1C: Details of Road Investments and Progress Status

Table 1: Summary of SURP II Road Investments

Progress Status	KM	%
Total Completed	32.34	33
Total ongoing roads	9.90	10
Total under Procurement	14.96	15
Total planned (<i>designs ready</i>)*	39.48	41
Total expected at end of Project	96.68	100

**Designs for all other cities are ready except for Baidoa 9km gravel road which will be ready by Mar '25.*

Table 2: Road Investments: Progress status by City

City	Road Investment	Total Km	Completed, Km	Works Ongoing	Procurement stage
Mogadishu		0.23	0.23	-	-
	Community road	0.23	0.23	-	0
Baidoa		21.25	14.70	-	6.55
	Package 1&2	14.70	14.70	-	0
	Package 3	6.55	-	0	6.55
Kismayo		22.11	8.30	8.70	5.11
	Package 1&2	17.00	8.30	8.70	0
	Package 3	5.11	-	0	5.11
Garowe		10.31	9.11	1.20	-
	Package 1&2	9.11	9.11	-	0
	VO	1.20	-	1.20	
Dhusamareeb		3.30	-	-	3.30
	Package 1	3.30	-	-	3.30
Total length, Km		57.20	32.34	9.90	14.96

Table 3: Road Investments: Planned under AF3 (designs ready)

City	Investment	Km	%
Mogadishu	4 road packages	12.83	32
Baidoa*	1 road package	9.00	23
Garowe	1 road package	2.00	5
Dhusamareeb	2 road packages	6.40	16
Beledweyne	3 road packages	9.25	23
Total planned roads		39.48	100

**Preparation of designs will start in Dec '24 and will take 4 months to complete.*

Annex 1D: ESF Agreed Next Steps

ESF			
1	Secure escrow account compensation funds, compensate PAPs physically and/or economically displaced by project activities.	PCU/PIUs	Before contract mobilization.
2	Include contractor labor recruitment plan in bidding documents.	PCU/PIUs	Continuous
3	Strengthen the capacity of female Community Engagement Officers, e.g. through certification.	PCU/PIUs	Continuous
4	Conduct cross-city learning exchange trips.	PCU/PIUs	Continuous
5	Implement the inclusion action plan under annex 6 to ensure women, youth, PWDs and other disadvantaged groups access project benefits such as employment and upskilling.	PCU/PIUs	Continuous
6	Ensure the design of sub-projects such as roads includes appropriate /feasible paths/routes to access households/facilities, as agreed upon with communities and their leadership.	PIUs	Continuous
7	UNOPS to submit quarterly reports on OHS inspections that are carried out weekly by E&S officer, showing details of compliance with EHS guidelines at construction sites, and details of any sanctions against recalcitrant contractors.	UNOPS through PCU	Quarterly every year
8	PCU, PIU and IoM to proactively inspect the shelters in Baidoa, to ensure any structural challenges are promptly addressed, to ensure that activities under the forced displacement component are concluded with no pending E&S obligations, including grievances.	PCU/PIU/IoM	Immediate

Annex 2: Disbursements

Total disbursement is US\$120 million or approximately 48% of total US\$253.5 million. Disbursement trend increased over time.

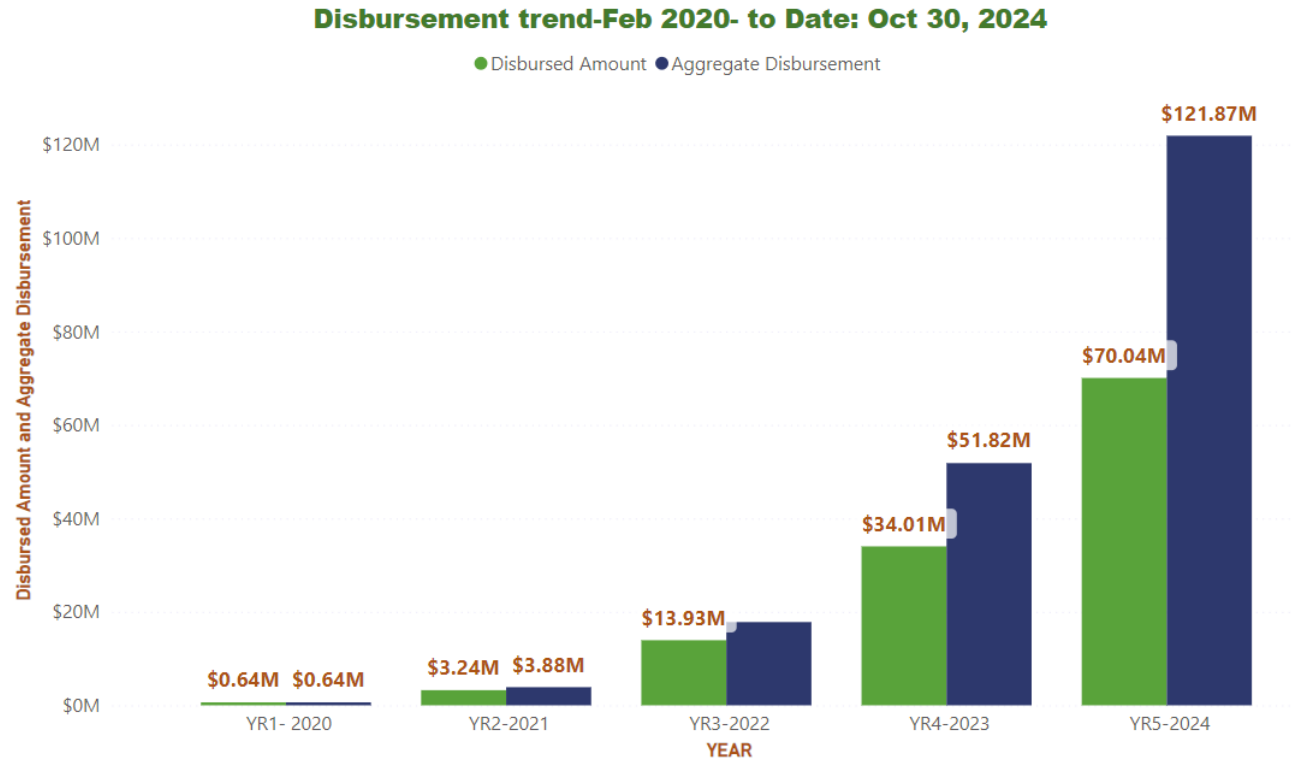


Table 1. Disbursement as of November 06, 2024 (in US\$)									
Grant no.	IDA D5310	IDAE0520	IDAE1490	IDAE3110	TFB1409	TFB1519	TFB8532	TFC4364	Total
Original Amount	50,000,000	20,000,000	50,000,000	40,000,000	45,000,000	17,000,000	21,500,000	10,000,000	253,500,000
Current amount	48,529,511	19,702,717	51,570,870	39,934,366	45,000,000	17,000,000	21,500,000	10,000,000	253,237,464
Exchange difference	1,470,489	297,283	(1,570,870)	65,634	-	-	-	-	262,536
Disbursed	25,896,774	42,616	45,031,101	-	42,609,120	6,557,144	-	-	120,136,755
Undisbursed	22,632,737	19,660,102	6,539,769	39,934,366	2,390,880	10,442,856	21,500,000	10,000,000	133,100,709
Disbursement rate	51.79%	0.21%	90.06%	0.00%	94.69%	38.57%	0.00%	0.00%	47.39%

Annex 3: MTR Assessment on Project Design

Relevance. The PDO of the project is “to strengthen public service delivery capacity of local governments, increase access to climate-resilient urban infrastructure and services, and to provide immediate and effective response to an eligible crisis or emergency in selected areas.” The PDO and its indicators remain highly relevant and achievable and should be retained. The project aims to provide 1 million people with improved access to climate-resilient urban infrastructure and services and has already exceeded 1 million beneficiaries reached under the municipal drought response, of which a significant proportion are women and IDPs.

The relevance for SURP-II remains high particularly in light of the El Niño Southern Oscillation (ENSO), which influences Somalia’s climate variability, bringing more rainfall and flooding during El Niño and droughts in La Niña years.²³ Climate-related shocks are occurring in increasingly quick succession, leaving little time for Somalis to recover.²⁴ During the MTR, the SURP-II mayors highlighted the significance of the project for increasing urban resilience to climate and disaster risks, especially flooding through drainage infrastructure investments and analytics that have helped prioritize Flood Risk Mitigation (FRM) investments. The mayors expressed demand for further support to strengthen urban resilience, including improving the capacity of municipal land administration departments and increasing the skills of local government functions on urban planning.

Expected outputs and results of the project, particularly the PDO indicators are gaining momentum. Three of the four PDO-level indicators are either on track or already surpassed. The only indicator that has been lagging is on total people with improved access to climate-resilient urban infrastructure and services. Beneficiaries are only counted when a sub-project has been completely handed over. The target for this indicator was substantially increased with the third additional financing to factor in additional sub-projects that had not been included in the original project. As of the latest estimates, 489,899 people have benefitted from completed works, which stands at 49% of the end target of 1,000,000. Given the scale of works ongoing, under procurement and in the pipeline, the indicator is expected to be achieved by project closing date.

Achievements

At the time of the MTR, the project has accomplished the following:

1. **Three additional financing, with total project amount of US\$253.5m.** The project has pioneered approaches like municipal-led implementation, use of country system, inter-governmental fund transfer, participatory planning, economic inclusion, capacity building and analytical works that have tangibly strengthened the public service delivery capacity of local governments while increasing access to climate-resilient urban infrastructure and services.
2. **The use of country system and implementation at municipal level.** This is one of the achievements under the project. The mission acknowledged ownership by the cities on investments completed and ongoing activities under the project. The allocation formula and transfer system

²³ Adelphi. Weathering Risk: Climate Risk Profile Somalia. 2023.

²⁴ GFDRR. Somalia Country Profile. Accessed in 2023.

¹² Climate Analytics. From droughts to floods: how Eastern

which follows the government system has become a good example of making development works in Somalia cities. It is expected that the cities through support from PCU, PIUs, and the MPWRH, will prepare of the O&M and sustainability plan prior to the project closing date.

3. **Strengthened government capacity at all levels.** Strong public service delivery and increasing access to climate-resilient urban infrastructure and services depend on good inter-governmental coordination and capacity. SURP-II has been able to build capacity at the municipal, federal member state, and federal levels of government in Somalia across different functions including engineering, contract management, and M&E. Some of the most The Somali Mayors Forum and engineering exchange in Sri Lanka were particularly notable in that they promoted greater dialogue and understanding across cities and different levels of government.
4. **City-wide urban analytics have led to more targeted investments.** Flood risk management diagnostics identified US\$230 million in FRM investment needs in Kismayo and US\$120 million for Garowe. The studies equipped the municipalities with the evidence needed to strategically prioritize drainage investments and provided a basis to engage with donors and other developing partners.
5. **Tangible civil works impacts.** The first two packages have been completed for 3 cities, and more are under preparation. To date, across Baidoa, Garowe, Kismayo, and Mogadishu 31.67 km or road length have been completed with 26.56 km in roadside drainage completed. Such investments have increased accessibility to services, including schools, hospitals, and markets. Additionally, business expansion has already been seen along improved roads with small businesses and vendors reporting increased customer traffic. And drainage systems have been proven to mitigate flood risks, reduce health risks, and improve public hygiene. The remaining cities have completed the feasibility and designs for their investments, with implementation expected to being early next year. The drought response delivered through IOM has significantly exceeded the target of beneficiaries reached by 285%.

Annex 4: Impact Assessment Reports

BAIDOA PROJECT IMPACT ASSESSMENT REPORT

1. Introduction

The Nagaad/SURP-II Project, funded by the World Bank, is a transformative initiative aimed at enhancing public service delivery, expanding climate-resilient urban infrastructure, and supporting rapid crisis response across six cities in Somalia. This project focuses on bridging critical infrastructure gaps while improving living conditions for both host communities and internally displaced persons (IDPs) in these urban centers.

In preparation for the Midterm Review (MTR) of the Nagaad Project, Key Informant Interviews (KIIs) were conducted with community leaders, government officials, project staff, and beneficiary group representatives in Baidoa. The primary purpose of these interviews is to gather qualitative insights into the project's impact, challenges, and areas for improvement. This qualitative data will be used alongside quantitative data from the project's Management Information System (MIS) to build a comprehensive assessment of the project's performance and impact.

2. Stakeholder Information

To ensure a well-rounded perspective on the project's impact, a diverse range of stakeholders was interviewed, including:

City	Group	Position	Number of People Interviewed
Baidoa	Local Government	Mayor	1
Baidoa	Local Business	Market Vendor	2
Baidoa	Community Organization	Youth Leader	1
Baidoa	Community Member	Resident	3
Total			7

Interview Methodology: Each interview lasted 30-45 minutes, covering topics ranging from infrastructure impact to community satisfaction. Interviews were conducted confidentially in Somali, with responses translated as needed to ensure clarity and accuracy. Interviewers documented responses thoroughly to provide a reliable qualitative foundation for the MTR.

3. Impact of Infrastructure Improvements

The infrastructure improvements under the Nagaad/SURP-II Project have yielded several tangible benefits for Baidoa's residents. These enhancements have not only improved access to essential services but have also positively impacted local businesses, community well-being, and safety.

Roads and Accessibility

- **Improved Market Access and Economic Activity:** The construction of new roads, such as Ali Amhar and Hospital Road 1B, has significantly boosted access to local markets like Muuri Market. Previously isolated by rough, unpaved paths, these markets now benefit from

increased foot traffic and smoother transport of goods, promoting local commerce and creating economic opportunities.

- **Enhanced Connectivity and Reduced Travel Times:** Road improvements have cut down travel times, especially for residents on the city's outskirts, including IDP camps. With more direct routes and better road quality, community members now experience easier and faster access to schools, healthcare facilities, and other services.
- **Expanded Emergency Response Capabilities:** The improved road network has facilitated faster emergency responses, as ambulances and other emergency vehicles can reach critical locations more quickly, contributing to enhanced public safety.

Drainage Systems

- **Flood Risk Mitigation:** Upgraded roadside drainage systems have been essential in reducing the frequency and severity of flooding, particularly during seasonal rains. These systems channel rainwater away from residential areas and roads, effectively managing water flow and reducing potential hazards.
- **Efficient Water Management and Community Resilience:** The drainage improvements have also fostered a greater sense of community confidence and resilience. Residents report feeling safer during heavy rains, knowing that flooding risks have been mitigated, allowing for continued mobility and economic activity.

Street Lighting

- **Improved Night Safety and Extended Business Hours:** The installation of solar streetlights has transformed nighttime safety and mobility. With well-lit streets, residents feel more comfortable moving around after dark, and local businesses have extended their hours, contributing to an active evening economy.
- **Reduction in Crime and Increased Community Activities:** Increased lighting has led to a noticeable drop in crime rates, as well-lit areas deter illegal activities. Additionally, residents now gather for social activities in the evenings, creating a more connected and vibrant community environment.

Pedestrian Walkways

- **Enhanced Safety for Vulnerable Groups:** Dedicated pedestrian walkways have significantly improved safety for those who previously shared roads with vehicles. Vulnerable groups, including children and the elderly, now have safer spaces for movement, reducing accident risks.
- **Increased Mobility and Promotion of a Healthier Lifestyle:** With walkways available, residents have adopted healthier habits, incorporated walking and jogging into their daily routines, which has led to a shift towards a more health-conscious and socially engaged community.

4. Community Perception and Satisfaction. The community in Baidoa has expressed a largely positive response to the SURP-II infrastructure developments, highlighting improved connectivity and quality of life. However, certain areas have been identified where adjustments could further enhance the project's impact:

- **General Satisfaction Levels:** Community members appreciate the ease of transportation and access to essential services. The new roads and walkways have been particularly beneficial in improving mobility and social interactions.

Areas for Improvement:

- **Road Extensions and Width:** Residents note that some roads could be widened or extended to accommodate higher traffic volumes, especially in areas experiencing rapid population growth.
 - **Closed Drains for Safety:** Open roadside drains, while effective in flood management, pose a safety risk to pedestrians and animals. The community has recommended covering drains to enhance safety.
 - **Maintenance Needs:** Regular maintenance of roads, walkways, and drainage systems has been emphasized as essential for sustaining the infrastructure's benefits.
6. **Livelihood and Economic Impact.** The infrastructure improvements have contributed significantly to local economic growth and improved livelihoods for Baidoa's residents. Key economic impacts include:
- **Increased Job Opportunities:** The construction phase created numerous jobs for residents, including skilled and unskilled positions. The increase in employment not only provided income but also allowed workers to acquire valuable skills for future projects.
 - **Boosted Local Businesses and Reduced Transportation Costs:** Improved roads have made it easier for vendors and small businesses to transport goods, reducing costs and expanding their customer base. As a result, there is more local commerce, and residents have more accessible shopping options.
 - **Impact on Public Transport and Property Values:** The development of smoother, reliable roads has led to fewer breakdowns of popular public transport options, such as Bajajs, enhancing efficiency and affordability for daily commuters. Additionally, property values have risen in areas close to the newly constructed roads, further incentivizing investment in these neighborhoods.
7. **Beneficiaries and Inclusivity.** The SURP-II Project has successfully reached a broad range of beneficiaries within Baidoa, with specific groups reporting substantial improvements in their daily lives:
- **Identification of Beneficiary Groups:**
 - **Residents and Local Community:** General public benefits from increased safety, improved infrastructure, and reduced travel times.
 - **Local Businesses and Entrepreneurs:** Enhanced access to customers and a more favorable environment for business operations.
 - **Local Government:** Infrastructure improvements have aided the local government in providing better services and addressing community needs effectively.
 - **Special Impact on Vulnerable Groups:**
 - **Internally Displaced Persons (IDPs):** Many IDPs, particularly women and youth, now have improved access to markets, healthcare, and social services, which has fostered integration into the urban community.
 - **Women and Youth:** Better connectivity has enabled NGOs and support agencies to deliver services more effectively, particularly to women and young people, who often face mobility constraints.

8. **Regional Influence and Wider Impact.** The impact of the infrastructure improvements extends beyond Baidoa, serving as a model for urban development in neighboring areas and motivating other towns to invest in similar projects:
- **Influence on Neighboring Towns and Regions:** Surrounding towns like Hudur and Berdale have started their own infrastructure projects, inspired by Baidoa's progress. By building gravel roads and improving local infrastructure, these towns aim to replicate Baidoa's development success.
 - **Examples of Replication Efforts:** The visible improvements in Baidoa have increased advocacy from other regions, prompting them to seek donor support and partner with development agencies for similar projects. The SURP-II project has therefore set a precedent, encouraging a ripple effect of urban development across the region.
9. **Challenges and Lessons Learned.** The implementation of SURP-II's infrastructure projects in Baidoa faced several challenges, which also provided valuable lessons for future initiatives:

Key Challenges:

- **Disruption of Public Utilities:** Road construction work occasionally impacted water pipes, electricity lines, and communication cables, leading to temporary service interruptions for residents and businesses.
- **Environmental Concerns:** Dust, noise, and waste generated during construction affected air quality and contributed to pollution, especially in dry periods. Mitigation measures, like water spraying for dust control, were implemented but posed ongoing management challenges.
- **Construction-Related Road Closures:** Temporary Road closures were necessary during construction, causing inconvenience for residents and disrupting local businesses. Although alternative routes were provided, these disruptions impacted daily activities.
- **Encroachment Issues:** Some structures built close to road reserves required removal or adjustment, resulting in delays and necessitating compensation arrangements.

Lessons for Future Projects:

- **Community Involvement in Planning:** Early and continuous engagement with community members helped build trust and reduce friction, making it clear that projects of this scale may involve temporary inconveniences for long-term benefits.
- **Proactive Utility Coordination:** Improved coordination with utility providers from the start can help prevent service disruptions, ensuring smoother project timelines and less disruption to the community.
- **Importance of Public Awareness Campaigns:** Educating residents about the project timeline, benefits, and temporary disruptions can enhance community patience and understanding, easing the implementation process.
- **Urban Planning and Zoning Compliance:** Setting and enforcing clear guidelines on road reserves and building encroachment can help prevent delays and community disputes in future infrastructure projects.

10. Recommendations for Improvement

Infrastructure Needs:

- **Box Culverts for Flood-Prone Areas:** Installing box culverts in locations prone to seasonal flooding can improve accessibility and reduce waterlogging issues.
- **Additional Roads and Streetlights:** Expanding Road networks and installing streetlights in other areas would ensure broader coverage, improving both safety and mobility.
- **Vocational Training Centers and Community Facilities:** Establishing training centers would provide residents with skill-building opportunities, contributing to long-term community development.
- **Enhanced Water Management Systems:** Improved water catchment areas and drainage facilities would support sustainable water management, especially important in high-rainfall seasons.

Community and Government Roles in Sustainability:

- **Local Involvement in Infrastructure Maintenance:** Encouraging community members to participate in infrastructure upkeep promotes a sense of ownership and responsibility.
- **Traffic Awareness and Road Safety Programs:** Educating the public on road safety practices, speed limits, and pedestrian crossing use will ensure that infrastructure is used safely and efficiently.
- **Immediate Response Protocols:** Establishing procedures for quick repairs of road damage or drainage blockages can prevent further infrastructure degradation and ensure consistent functionality.

11. Conclusion. The Nagaad/SURP-II infrastructure projects have brought significant improvements to Baidoa's urban environment, enhancing accessibility, safety, and economic growth. These developments have not only improved quality of life but also served as a model for surrounding regions, showcasing the positive impact of targeted urban resilience projects. Looking forward, the focus will remain on expanding infrastructure coverage, sustaining project outcomes, and enhancing community involvement to ensure long-term success. Continued collaboration between the community, local government, and development partners will be key to building on the progress achieved and addressing emerging urban challenges.

GAROWE SURP-II PROJECT IMPACT ASSESSMENT REPORT

1. Introduction. The Nagaad/SURP-II Project, funded by the World Bank, focuses on enhancing public service delivery, expanding access to climate-resilient urban infrastructure, and bolstering community resilience across key Somali cities, including Garowe. This initiative is part of a larger effort to support urban infrastructure development that addresses the needs of both host communities and internally displaced persons (IDPs). In Garowe, the project has implemented new road networks, roadside drainage systems, pedestrian walkways, and solar streetlights, aiming to improve connectivity, safety, and accessibility for residents. To gain insight into the project's impact, Key Informant Interviews (KIIs) were conducted with various stakeholders, including local government officials, business owners, and residents, as part of the Midterm Review (MTR). These interviews provide qualitative data to complement quantitative findings from project reports, enabling a holistic understanding of how the project has influenced community well-being and economic activities.

2. Stakeholder Information. A range of stakeholders was interviewed to capture diverse perspectives on the project's impact:

City	Group	Position	Number of People Interviewed
Garowe	Local Government	Deputy Mayor	1
Garowe	Local Business	Shop Owner	2
Garowe	Community Member	Resident	2
Total			5

Interview Methodology: Each interview lasted approximately 30-45 minutes and was conducted in Somali, with responses translated as needed. The responses were documented to provide an in-depth view of the infrastructure improvements' impact on daily life, community safety, and economic growth in Garowe.

3. Impact of Infrastructure Improvements. The infrastructure developments implemented under the SURP-II Project in Garowe have yielded several significant benefits for the city's residents, enhancing accessibility, safety, and economic vitality. Key areas of impact include:

- **Roads and Accessibility**
 - **Improved Access to Services:** The construction of new roads, such as Towfiq and 30th Street, has facilitated smoother access to essential services, including schools, healthcare facilities, and markets. Residents reported substantial reductions in travel times and the increased availability of transportation options, such as Bajaj services, which have become more widespread following road improvements.
 - **Enhanced Economic Activity:** The improved road network has attracted new businesses along these routes, creating job opportunities and promoting economic growth. Shops, cafes, and other small businesses have benefited from increased foot traffic, while property values along these roads have risen, encouraging further investment.
 - **Safety and Emergency Response:** Better roads have contributed to improved emergency response times, with emergency vehicles able to reach affected areas more quickly and safely. Additionally, reduced road roughness has lowered vehicle wear and tear, further supporting reliable access to essential services.
- **Drainage Systems**

- **Flood Prevention:** The implementation of roadside drainage systems has significantly reduced the risk of flooding along major roads, especially in areas like Towfiq Street. These drainage channels ensure smoother water flow during the rainy season, minimizing road damage and protecting surrounding properties.
- **Improved Sanitation and Road Longevity:** The drainage infrastructure has improved local sanitation by preventing water stagnation and erosion, enhancing the long-term durability of the road network and creating cleaner, more resilient urban spaces.
- **Street Lighting**
 - **Nighttime Safety and Crime Reduction:** Solar-powered streetlights installed along major roads have enhanced nighttime visibility, reduced crime rates and improving safety for residents. Many community members, especially women and youth, feel safer traveling at night, and local businesses have been able to extend their operating hours, supporting a more active evening economy.
 - **Increased Community Mobility:** The lighting has encouraged community activities after dark, allowing residents to move freely and safely around the city in the evenings and fostering a stronger sense of community.
- **Pedestrian Walkways**
 - **Increased Mobility and Health Benefits:** The newly installed pedestrian walkways have improved mobility for pedestrians, particularly vulnerable groups such as children and the elderly. These walkways provide safe, dedicated paths, encouraging walking as a mode of transport and supporting healthier, more active lifestyles.
 - **Enhanced Community Connectivity:** With these walkways, community members are now better connected, and pedestrian safety has greatly improved, reducing the risk of road accidents and enhancing the overall walkability of the city.

4. Community Perception and Satisfaction. The feedback gathered from Garowe residents indicates strong community approval of the SURP-II infrastructure improvements, with key areas highlighted as follows:

- **General Satisfaction:** Community members expressed positive perceptions of the infrastructure developments, appreciating improved mobility, safety, and economic opportunities. The enhancements in road conditions and street lighting have increased community morale, with residents hopeful for continued urban progress.
- **Areas for Improvement:**
 - **Broader Drainage Improvements:** While the drainage systems have reduced flooding along main roads, residents noted that further improvements could benefit additional areas prone to waterlogging. Improved cleaning and maintenance protocols were suggested to ensure optimal drainage performance.
 - **Green Spaces and Beautification:** Some residents expressed a desire for more greenery along the newly developed roads. This includes planting trees or shrubs that would enhance the visual appeal of these spaces, contributing to environmental benefits and community well-being.

5. Livelihood and Economic Impact. The SURP-II infrastructure improvements have fostered economic growth and expanded livelihood opportunities within Garowe, enhancing residents' quality of life and business prospects:

- **Increased Job Opportunities:** The construction and maintenance phases of the project generated local employment, offering job opportunities that ranged from skilled labor in construction to maintenance roles. This influx of jobs has positively impacted the local economy, helping residents improve their livelihoods.
 - **Enhanced Business Environment:** With improved roads and pedestrian access, local businesses have experienced an increase in customer traffic. The upgraded road network has enabled more efficient goods transport, while cafes, shops, and service providers have reported growth in clientele, contributing to an active local economy.
 - **Reduction in Travel and Transport Costs:** Enhanced connectivity and safer roads have made daily commutes more efficient and affordable, with businesses saving on transportation costs and residents finding it easier to access essential services and employment centers.
7. **Beneficiaries and Inclusivity.** The SURP-II Project in Garowe has reached a wide array of beneficiaries, with positive impacts noted for vulnerable groups:
- **Key Beneficiary Groups:**
 - **Residents and Business Owners:** Property owners along the newly constructed roads have benefited from increased property values, while businesses have thrived due to higher foot traffic and enhanced accessibility.
 - **Vulnerable Groups:** Women, children, the elderly, and IDPs have particularly benefited from safer pedestrian pathways, improved road access, and enhanced security measures, such as street lighting. These improvements have contributed to greater social inclusion and access to resources.
 - **Community-Wide Benefits:** The improved infrastructure has provided all residents, regardless of socio-economic status, with enhanced access to public spaces and services, promoting inclusivity and broader community cohesion.
8. **Regional Influence and Wider Impact.** The infrastructure developments in Garowe have also had positive effects beyond the immediate project area, influencing neighboring communities and setting a model for further urban development:
- **Increased Inter-Regional Connectivity:** New roads have facilitated easier travel for vehicles carrying goods across regions, supporting broader trade and improving supply chain efficiency in and around Garowe .
 - **Model for Other Regions:** The success of Garowe’s infrastructure improvements has encouraged nearby towns to seek similar developments, with some areas looking to replicate these projects and enhance their own urban environments. This cross-regional interest underscores the broader impact of the SURP-II Project as a catalyst for urban development.
9. **Challenges and Lessons Learned.** The implementation of the SURP-II infrastructure projects in Garowe encountered some challenges, which provided key insights and lessons to guide future projects:
- **Key Challenges:**
 - **Utility Disruptions:** During construction, utility services such as water and electricity were occasionally disrupted, affecting residents and businesses. Improved pre-planning and coordination with utility providers could mitigate these issues in future projects.

- **Temporary Inconveniences:** Road closures, dust, and noise during construction were noted as temporary inconveniences for the community. These disruptions, though managed with alternative routes, impacted daily activities, particularly for residents in affected areas.
- **Maintenance Needs for Drainage Systems:** Some stakeholders expressed concerns about the long-term maintenance of drainage systems to ensure consistent flood prevention. Establishing regular cleaning and monitoring routines was highlighted as essential for sustaining the system's effectiveness.
- **Lessons for Future Projects:**
 - **Community Engagement is Vital:** Early and regular communication with residents increased their understanding and acceptance of temporary inconveniences, building trust and fostering a sense of community involvement.
 - **Better Utility Coordination:** Collaborating with utility providers before project initiation helped minimize service disruptions, enabling smoother project execution.
 - **Documentation and Knowledge Sharing:** Capturing lessons learned and maintaining open communication channels among project teams and the local community ensured that challenges were addressed effectively and can be avoided in future projects.

10. **Recommendations for Improvement.** Based on community feedback and project outcomes, several recommendations were identified to enhance the impact and sustainability of Garowe's infrastructure improvements:

- **Infrastructure Needs:**
 - **Expanded Drainage and Greening Initiatives:** Expanding the drainage network to more areas and incorporating green spaces along major roads could further improve flood management and enhance the urban environment's visual appeal.
 - **Regular Maintenance Schedules:** Establishing systematic maintenance schedules for roads, drainage systems, and street lighting would preserve the quality and functionality of the infrastructure, ensuring longevity and reducing the risk of deterioration.
 - **Traffic and Pedestrian Safety Education:** Implementing safety campaigns to educate residents on safe road usage, pedestrian walkways, and traffic rules would support responsible infrastructure use and improve public safety.
- **Community and Government Roles in Sustainability:**
 - **Local Ownership and Accountability:** Encouraging community members to take an active role in reporting damage or maintenance needs would promote a shared sense of responsibility and preserve infrastructure quality.
 - **Collaborative Maintenance Programs:** Local government and community partnerships could support ongoing maintenance efforts, including cleaning, tree watering, and streetlight servicing, fostering a sustainable, well-maintained urban environment.

10. Conclusion. The SURP-II infrastructure projects in Garowe have significantly enhanced the city's accessibility, economic potential, and safety, creating a positive ripple effect throughout the community. The improved roads, drainage systems, walkways, and street lighting have transformed daily life for residents, reduced crime, and bolstered the local economy. Additionally, the success of these projects has set a model for neighboring areas, inspiring further urban improvements across the region.

Looking ahead, maintaining the infrastructure and expanding initiatives such as drainage and green spaces will be critical to sustaining these achievements. Through continued collaboration between the local government, community, and development partners, Garowe's infrastructure can continue to serve as a foundation for a resilient and prosperous urban future.

KISMAYO SURP-II PROJECT IMPACT ASSESSMENT REPORT

1. Introduction. The Nagaad/SURP-II Project, funded by the World Bank, aims to enhance urban infrastructure, public service access, and climate resilience across Somalia's key cities, including Kismayo. This project is particularly focused on improving the lives of both host communities and internally displaced persons (IDPs) through the construction of climate-resilient roads, pedestrian walkways, drainage systems, and solar streetlights. In Kismayo, these improvements aim to increase mobility, safety, and economic opportunity while fostering community development and resilience. As part of the Midterm Review (MTR) of the Nagaad Project, Key Informant Interviews (KIIs) were conducted with various stakeholders, including government officials, local business owners, and service providers, to assess the project's impact. The feedback collected provides valuable qualitative insights that complement quantitative data, capturing the project's impact on quality of life, local economic growth, and community safety in Kismayo.

2. Stakeholder Information. The following stakeholders in Kismayo were interviewed to gain a comprehensive understanding of the SURP-II project's impact:

City	Group	Position	Number of People Interviewed
Kismayo	Local Government	Mayor	1
Kismayo	Service Provider	Taxi Driver	1
Kismayo	Local Business	Small Business Owner	2
Kismayo	Community Member	Resident	3
Total			7

Interview Methodology: Each interview was conducted in Somali and lasted approximately 30-45 minutes. Responses were translated and documented, allowing a detailed view of infrastructure improvements and their effects on everyday life in Kismayo.

3. Impact of Infrastructure Improvements. The infrastructure improvements introduced under the SURP-II Project have had a transformative impact on Kismayo's residents, businesses, and overall city landscape. These developments have enhanced accessibility, increased safety, and bolstered economic activity across the city. The main areas of impact include:

- **Roads and Accessibility**
 - **Improved Access to Services:** The newly constructed and rehabilitated roads, such as those on Afmadow and 15 May Roads, have significantly improved access to essential services like schools, hospitals, and markets. Residents report faster, more reliable transportation options, with previously challenging routes now accessible for both private vehicles and taxis, allowing residents to reach these services with ease.
 - **Reduced Travel Time and Business Growth:** Improved Road conditions have drastically reduced travel times across the city, enhancing overall productivity. For example, travel to Suqyare Market now takes minutes instead of hours. This efficiency has spurred local business growth, with many new shops, markets, and supermarkets opening along the rehabilitated roads, benefiting from the increased customer footfall.

- **Safer and More Reliable Transportation:** Better roads have resulted in fewer vehicle breakdowns, which has particularly benefitted the local taxi industry. Drivers report substantial reductions in maintenance costs, as the improved infrastructure has allowed for safer, more reliable services, reducing wear and tear on their vehicles.
- **Drainage Systems**
 - **Effective Flood Prevention:** The roadside drainage systems have effectively reduced flooding during heavy rains, which previously created major challenges for residents and businesses. Areas like Argo and Calanley Road, once prone to severe flooding, are now flood-free, allowing for uninterrupted business operations and easier mobility for residents.
 - **Enhanced Sanitation and Health Benefits:** The improved drainage systems have also contributed to better environmental health by eliminating stagnant water, which previously posed risks of waterborne diseases. The efficient channeling of rainwater has created a cleaner, safer urban environment, directly benefited community health and reduced sanitation costs.
- **Street Lighting**
 - **Increased Nighttime Safety and Crime Reduction:** Solar-powered streetlights have vastly improved nighttime safety, reducing crime rates and creating a safer environment for residents and businesses. Community members, particularly women and youth, now feel more secure moving around at night, fostering a more active nighttime economy with extended business hours along these well-lit roads.
 - **Support for Local Businesses:** The availability of streetlights has allowed businesses to extend their operating hours into the evening. This shift has encouraged an increase in economic activity and nightlife, with local shops and cafes staying open later and attracting more customers, contributing to a vibrant city atmosphere.
- **Pedestrian Walkways**
 - **Enhanced Safety and Accessibility:** Dedicated pedestrian walkways have improved safety for walkers, particularly vulnerable groups like children and the elderly. These pathways have created clear, structured spaces for pedestrians, reducing the risk of accidents and encouraging a walking culture that promotes health and mobility for all residents.
 - **Social and Health Benefits:** Walkways have encouraged physical activity among residents, with many using these spaces for walking, jogging, and social gatherings. This has contributed to healthier lifestyles and stronger community bonds as residents are more likely to engage with each other in these safe, accessible public spaces.

4. Community Perception and Satisfaction. The community in Kismayo has responded positively to the SURP-II infrastructure improvements, highlighting the significant benefits the project has brought to everyday life. However, certain areas have been identified where additional enhancements could further increase community satisfaction.

- **General Satisfaction Levels:** Community members expressed high levels of satisfaction with the improved infrastructure, particularly the roads, drainage systems, and street lighting. Many residents noted the visible transformation in their neighborhoods, with improved mobility, safety, and business opportunities fostering a sense of pride in the city.
- **Areas for Improvement:**

- **Covered Drainage Systems:** Community members have requested that open drains be covered to reduce the risk of accidents involving pedestrians and animals. This adjustment could enhance overall safety, especially for children and elderly residents.
- **Beautification and Environmental Awareness:** Residents expressed a desire for more green spaces and tree planting along the main roads to enhance the city's aesthetics and promote environmental health. Additionally, increased community awareness initiatives were recommended to encourage residents to actively participate in maintaining the infrastructure.

5. Livelihood and Economic Impact. The SURP-II project has had a profound effect on local economic growth and livelihood opportunities in Kismayo. These improvements have helped expand businesses, create jobs, and increase property values across the city:

- **Job Creation and Business Expansion:** The new infrastructure has enabled local businesses to flourish, with new shops, markets, and eateries opening along the improved roads. This surge in commercial activity has created job opportunities, especially for youth, who now have more avenues for employment in the growing market.
- **Enhanced Accessibility for Essential Services:** Improved Road conditions have facilitated easier access to schools, healthcare facilities, and markets, which has enhanced daily life for residents. Travel times have been significantly reduced, allowing for faster and more efficient transportation across the city.
- **Increased Property Values:** Property values have increased along the new roads, with some areas experiencing rent hikes as businesses and residents move closer to the improved infrastructure. These economic shifts have contributed to community-wide economic vitality, benefitting both property owners and local entrepreneurs.

6. Beneficiaries and Inclusivity. The SURP-II Project in Kismayo has reached a broad range of beneficiaries, with benefits observed for vulnerable groups, including IDPs, youth, and women:

- **Primary Beneficiaries:**
 - **Residents and Business Owners:** The improved infrastructure has primarily benefited local businesses, residents, and property owners, who have seen enhanced accessibility and higher foot traffic in commercial areas.
 - **Vulnerable Groups:** The new infrastructure has been particularly impactful for women, youth, and internally displaced persons (IDPs). Women and youth have gained safer access to markets and social spaces, while IDPs now have better opportunities for employment and access to essential services due to the improved road network.
- **Community-Wide Benefits:** The infrastructure upgrades have fostered a sense of inclusivity and accessibility for all residents, encouraging a more connected and cohesive community. With enhanced safety and mobility, vulnerable groups have greater opportunities to participate in social and economic activities.

7. Regional Influence and Wider Impact. The positive outcomes of Kismayo's infrastructure improvements have extended beyond the city, influencing neighboring areas and inspiring similar initiatives:

- **Influence on Neighboring Towns:** The success of Kismayo's infrastructure projects has inspired nearby towns such as Afmadow and Dhobley to explore similar developments. These towns have

initiated consultations and begun preparations to upgrade their own roads and drainage systems, recognizing the benefits observed in Kismayo.

- **Examples of Regional Impact:** Kismayo's transformation has sparked interest from surrounding regions in replicating these improvements, with plans for community forums and consultations to discuss priority infrastructure needs. This regional influence highlights Kismayo's role as a model for urban development, promoting economic growth and infrastructure resilience across the broader region.

8. Challenges and Lessons Learned. While the SURP-II infrastructure improvements have brought positive changes to Kismayo, the project faced several challenges that offer valuable insights for future initiatives:

- **Key Challenges:**
 - **Disruptions During Construction:** Road closures and utility disruptions were significant challenges for residents and businesses during the construction phase. The closures affected daily routines, with limited alternative routes causing inconvenience for residents and local commerce.
 - **Dust and Noise Issues:** Dust and noise from construction activities presented environmental challenges, especially for those living and working near the construction zones. These issues temporarily affected air quality and disrupted the peace for nearby residents.
 - **Open Drains as Safety Hazards:** Although the new drainage systems have been effective in reducing flooding, open drains have raised concerns for pedestrian safety, with community members recommending that they be covered to prevent accidents.
- **Lessons for Future Projects:**
 - **Community Engagement in Planning:** Early and frequent communication with the community helped minimize resistance and ensured that residents understood the project's purpose. Ongoing consultations helped build trust and align project goals with community needs.
 - **Effective Management of Road Closures:** Enhanced coordination with local businesses and public services during road closures could mitigate the impact of disruptions, allowing better preparation for alternative routes and access points.
 - **Regular Maintenance Planning:** Establishing maintenance plans for drainage and road infrastructure during the planning stages helps ensure long-term project sustainability, minimizing the risk of deterioration over time.

10. Recommendations for Improvement. Based on community feedback and the experiences from the SURP-II project, several recommendations have been proposed to further enhance the benefits and sustainability of Kismayo's infrastructure improvements:

- **Infrastructure Enhancements:**
 - **Cover Open Drains:** Covering open drains would reduce safety risks for pedestrians and animals, especially in densely populated areas.
 - **Expand Greening Initiatives:** Planting trees along the main roads and adding green spaces could improve air quality, enhance visual appeal, and promote environmental awareness among residents.

- **Install Traffic and Pedestrian Signals:** Adding traffic lights and pedestrian crossings at key intersections would improve road safety, particularly for pedestrians, by creating clear, organized spaces for both vehicles and walkers.
- **Community and Government Roles in Sustainability:**
 - **Maintenance and Cleanliness:** Establishing a dedicated team to maintain roads, drainage, and green spaces could ensure that the infrastructure remains functional and visually appealing. This initiative could also create job opportunities for residents.
 - **Awareness Campaigns for Public Responsibility:** Running awareness campaigns to educate residents on infrastructure use, maintenance, and environmental cleanliness would encourage a sense of responsibility and community ownership of the improvements.

10. Conclusion. The SURP-II infrastructure projects have greatly benefited Kismayo, enhancing mobility, safety, and economic growth while improving the quality of life for residents. The construction of resilient roads, drainage systems, pedestrian walkways, and street lighting has fostered a more connected and secure community, with local businesses thriving and vulnerable groups gaining better access to essential services. Looking forward, continued collaboration between the local government, community members, and development partners will be essential to maintain and build upon these achievements. By implementing the recommendations and maintaining an inclusive approach, Kismayo can ensure long-term sustainability and serve as a model for similar urban resilience initiatives across the region. With the community's support, Kismayo's infrastructure improvements can remain a pillar of progress, supporting the city's development for years to come.

Annex 6: Inclusion of Women, Youth and Persons with Disabilities

Recommendation	Actions	Responsible	Timeline
Bidding documents, requirement for contractors to prepare, implement a Local Recruitment Plan (LRP).	Contractors to submit LRP in the bidding documents, showing how contractors will reach out, recruit and retain women, youth and Persons with Disabilities.	PIU	During the Bid
	Contractors to include indicators in ESHS metrics for measuring progress.	PIU	During the Bid
Promote inclusion of women, youth, and PWDs in employment and upskilling by setting targets in bidding documents.	• Skill training on PCIP for 70 women. Each city to train 10 except BRA which will train 20 women. This will be achieved through collaboration with Technical and Vocational Education and Training Centers (TVETs), requiring contractors to meet the LRP obligations. • Setting of an obligation for contractors to train/retrain young people -national talent, including a target for female talent, enhance local female and male capacity. • Safe employment, upskilling of PWDs, reporting on the progress.	PIU	Before Civil work started in each Sub project of the cities
Putting aside provisional sums to contractors against the agreed targets for employment of women, youth and PWDs. (Future).	Putting aside provisional sums to be paid to contractors against the agreed quantitative targets for women's employment (for future bidding).	PIU	During the preparation BOQ and bid evaluation report
Establish female role models by investing in and promoting experienced female workers on all levels related to Nagaad project.	Skills and career advancement trainings for Female staff with high potential.	PIU	Before civil work started
	Coaching and mentoring session young women professionals as engineers and technicians: • Engineers' internship, On Job Trainings to include women. • Upcoming Capacity building engineer at Federal, State and Municipal level should include women.	PIU	

